


CABOT ELEMENTARY SCHOOL PROJECT

Monthly Community Construction Project Update

May 2019

Thursday, May 9, 2019 - 6:30PM

Newton City Hall, Room 211

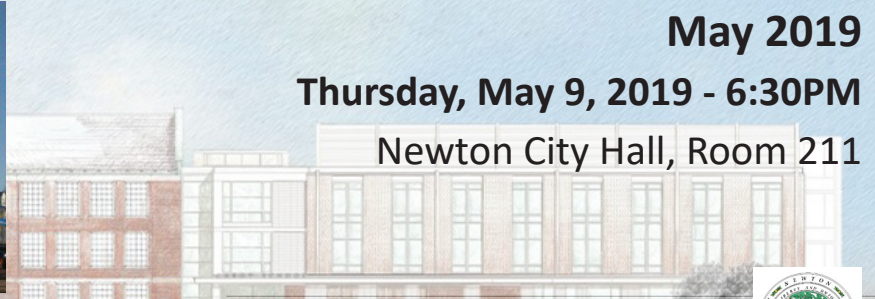

CONSTRUCTION ACTIVITIES

OVERALL CONSTRUCTION SCHEDULE



NOTE: SATURDAY WORK WILL CONTINUE TO BE PERFORMED OVER THE NEXT FEW MONTHS, BEGINNING AT 7:00AM.

Noise will be minimized as much as possible until 8:00AM.

- EXTERIOR BUILDING WORK -- Final windows installation is ongoing at the gym. Metal panel installation is ongoing at the classroom addition, library and gym. Thin brick installation is underway.
- EXTERIOR SITEWORK, SITE IMPROVEMENTS AND LANDSCAPING -- Conduit and bases for site lighting as well as the granite amphitheater are installed. School sign wall masonry is underway. Grading activities are on going. Curb and sidewalk activity along Bridges Ave are scheduled to begin on 5/09/19.
- INTERIOR WORK CLASSROOM ADDITION/1929 RENOVATION -- Resilient flooring and millwork installation are underway on the 1st floor. Corridor wall tile is substantially complete on the 1st floor. Millwork installation is complete on the 2nd and 3rd floors. Corridor wall tile is complete on the 2nd and 3 third floors. Epoxy flooring in the bathrooms complete. Toilet fixtures and finishes are installed in the bathrooms. Students locker installation is complete on the 3rd floor and substantially complete on the 2nd. Ceiling grid installation is underway on the 1st floor. Above ceiling inspections have been completed and signed off on the 3rd and 2nd floors.
- GYM -- GWB installation is complete at the high walls. Window installation should be complete in two weeks. Painting and installation of tectum sounds panels shall begin shortly. Gym equipment installation to begin mid may.
- LIBRARY -- Priming and painting has begun. Ceiling grid installation to follow painting. Millwork installation to follow installation of ceiling grid.



Spring 2018 - Fall 2018

Fall 2018 - Spring 2019

Spring 2019

Spring 2019 - Summer 2019

Fall 2019



Exterior Shell

Interior Fit Out

Substantial Completion

Landscaping; FFE; Technology

Occupy School



PROJECT CONSULTANT TEAM

NV5 - Owner's Project Manager
DiNisco Design - Architect
W. T. Rich Company - Construction Project Manager



CONTACTS

Alex Valcarce - City of Newton
Project Manager (617) 796-1600
For After Hours Emergencies - W. T. Rich Company (617) 467-6010

* General Cabot updates will be the 2nd Thursday of each month at 6:30PM for the project duration, unless otherwise noted.

For project updates, please visit: http://www.newtonma.gov/gov/building/cabot_school

For project webcams, please visit:

<http://108.26.191.186:9900/#view> (Bridges) -- <https://app.oxblue.com/open/wtrich/cabotschool> (Parkview)

Massachusetts School Building Authority



NV5

DINISCO DESIGN
architects + planners



W.T. RICH COMPANY, INC.

The location of this meeting is accessible and reasonable accommodations will be provided to persons requiring assistance. If you need a reasonable accommodation, please contact the city of Newton's ADA Coordinator, Jini Fairley, at least two business days in advance of the meeting: jfairley@newtonma.gov or (617) 796-1253. For Telecommunications Relay Service, please dial 711.
