

Cabot Elementary School

Newton, MA


Construction Sequencing Overview



W.T. RICH COMPANY, INC.


4/27/17

Site Circulation

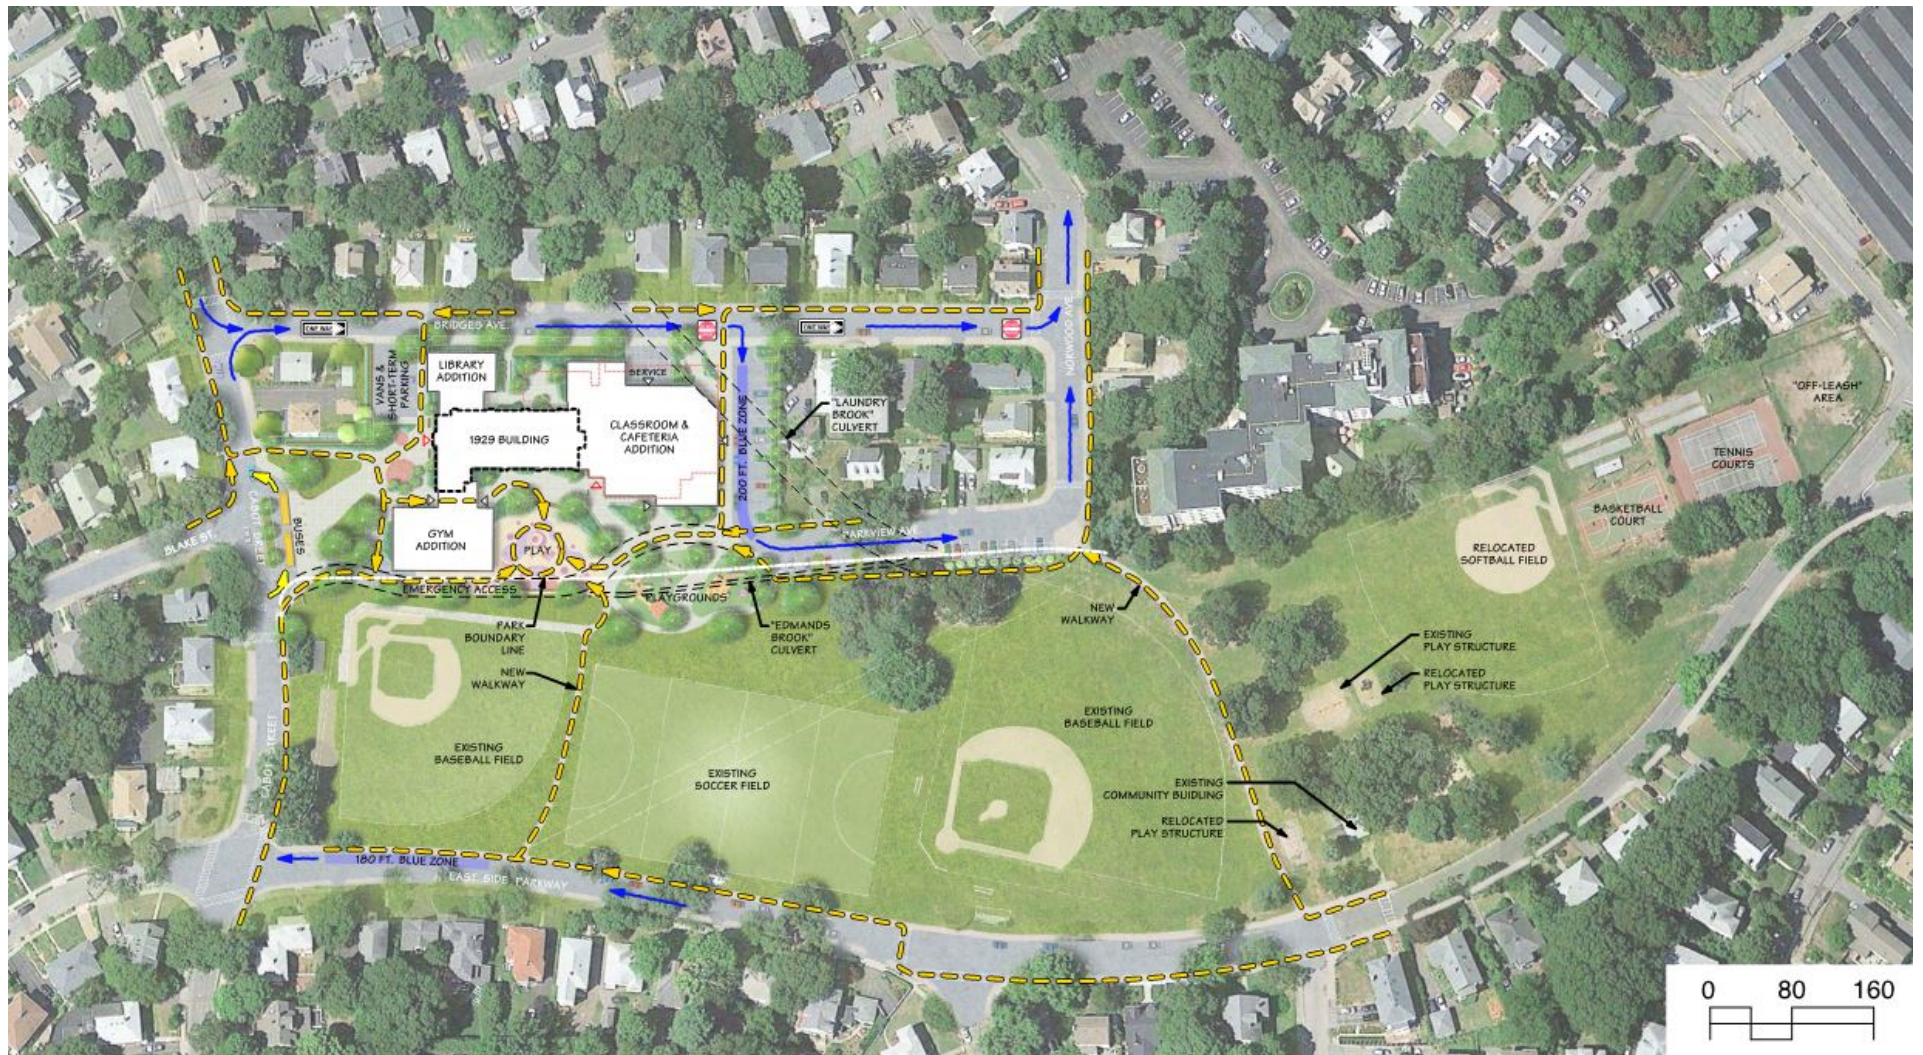


Site Mobilization: Setup Site Controls & Facilities

Early July 2017

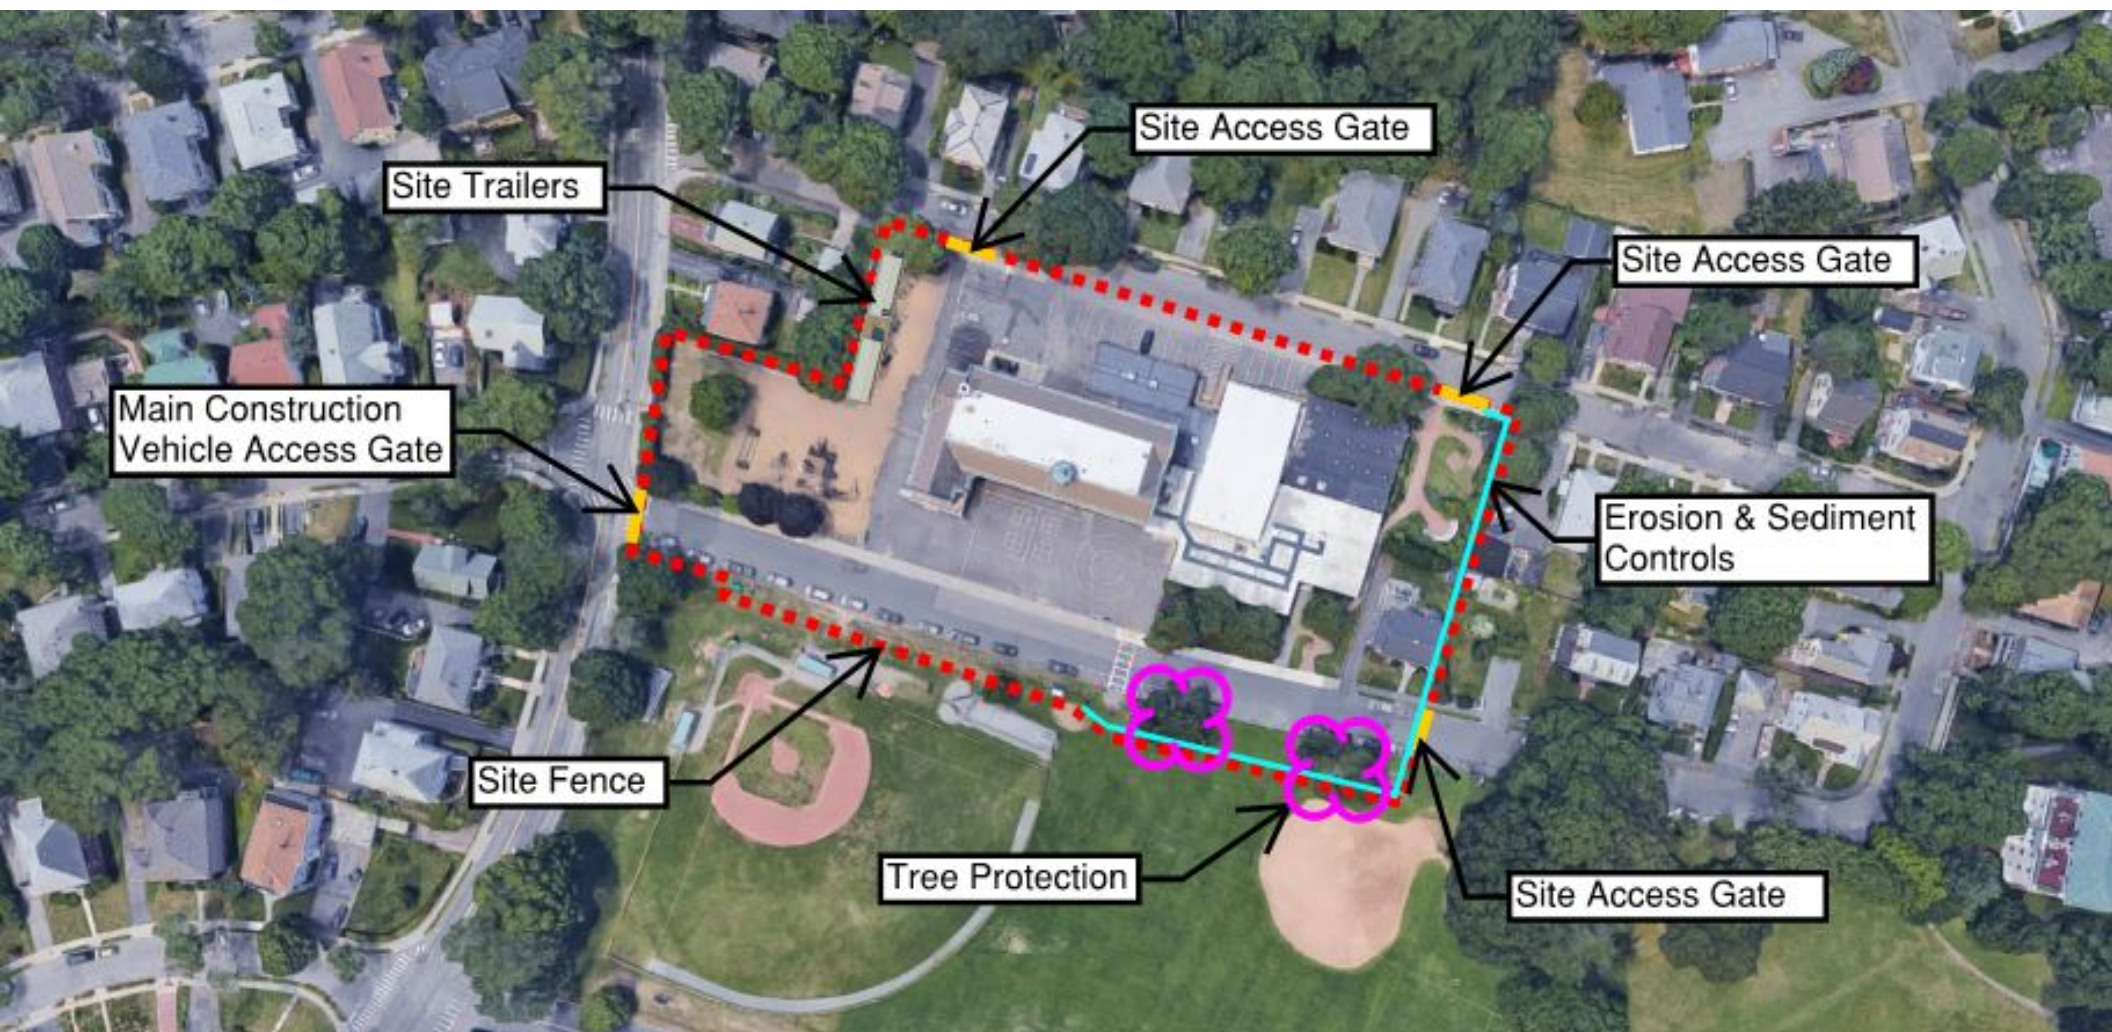


Traffic Signage: Setup Traffic Controls

Early July 2017

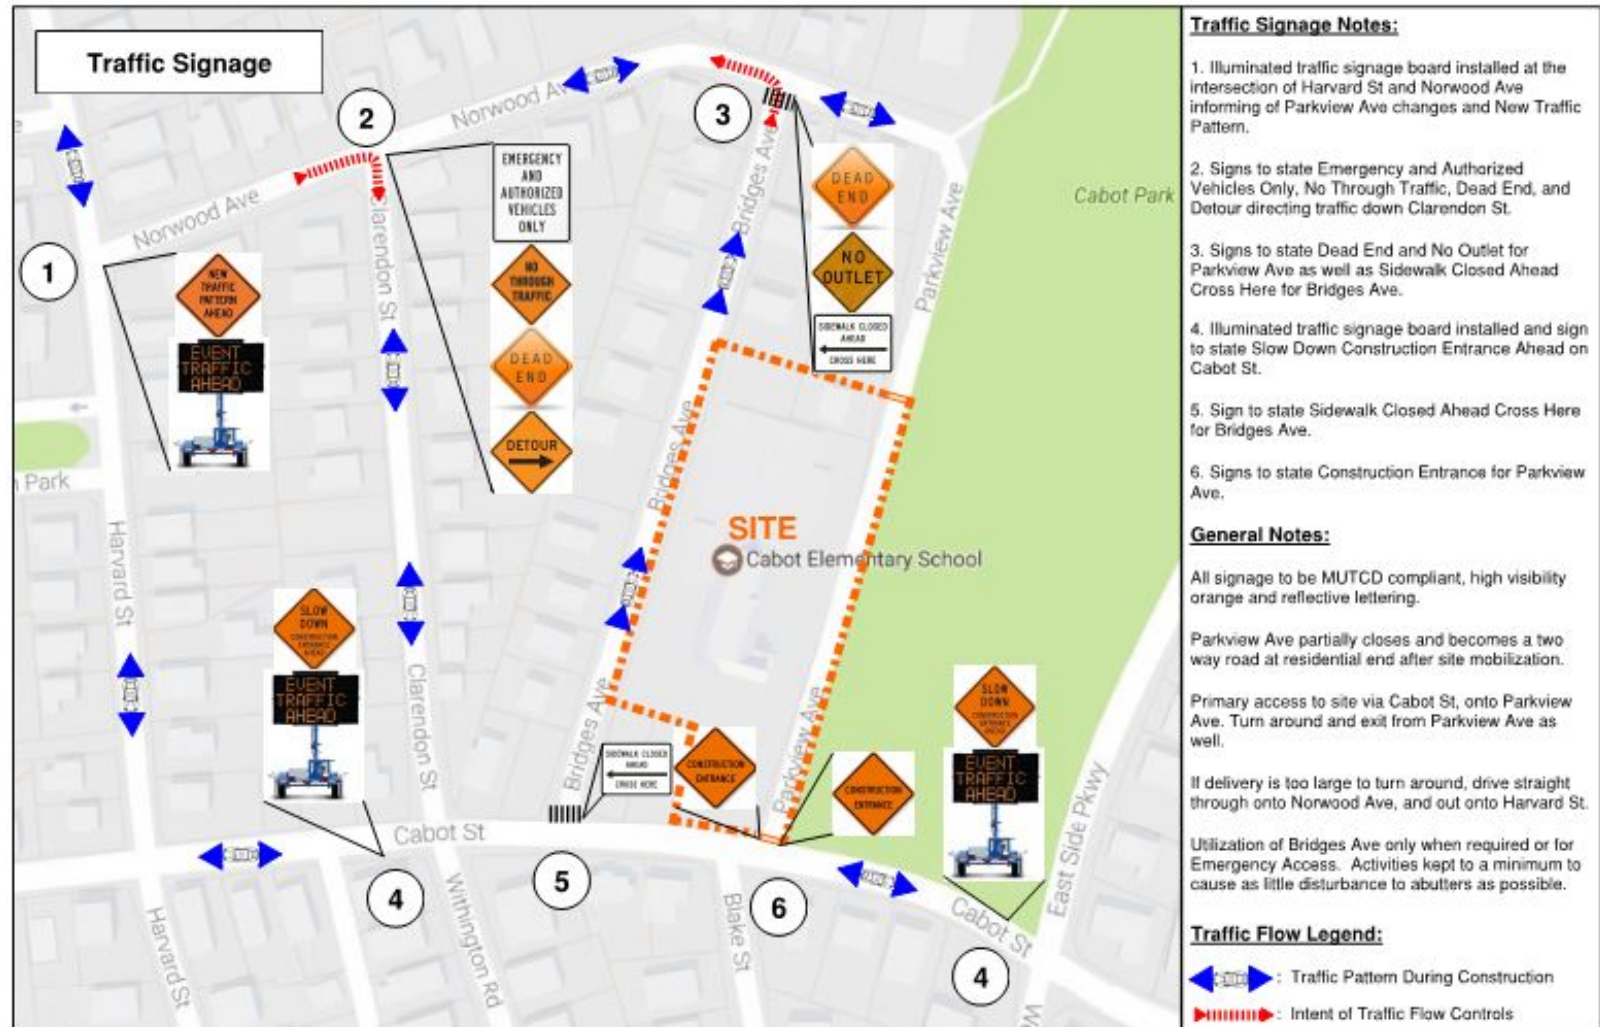


Stage 1: Demolition of Modular Classrooms, 23 Parkview, & Landscaping

Early July 2017

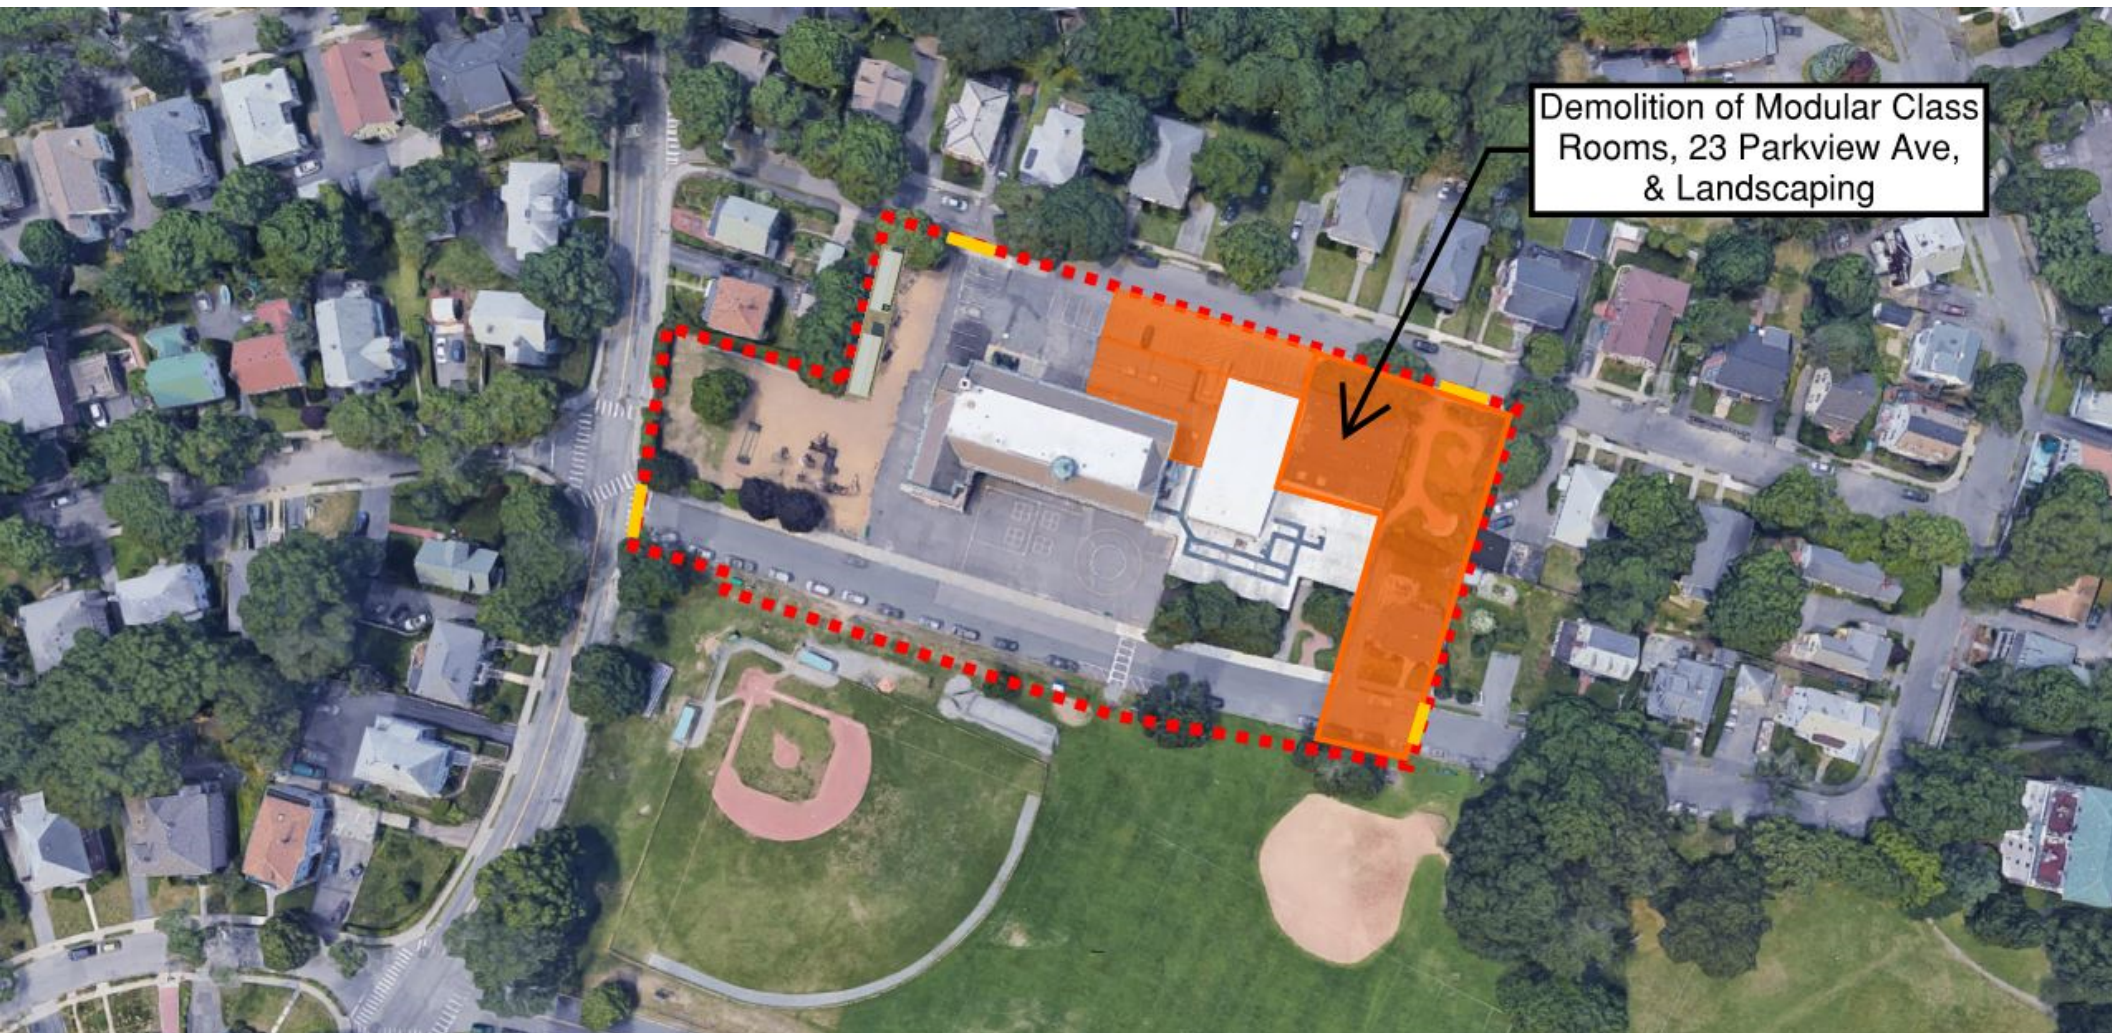

Stage 2: Demolition of 1956 Addition


Mid July 2017

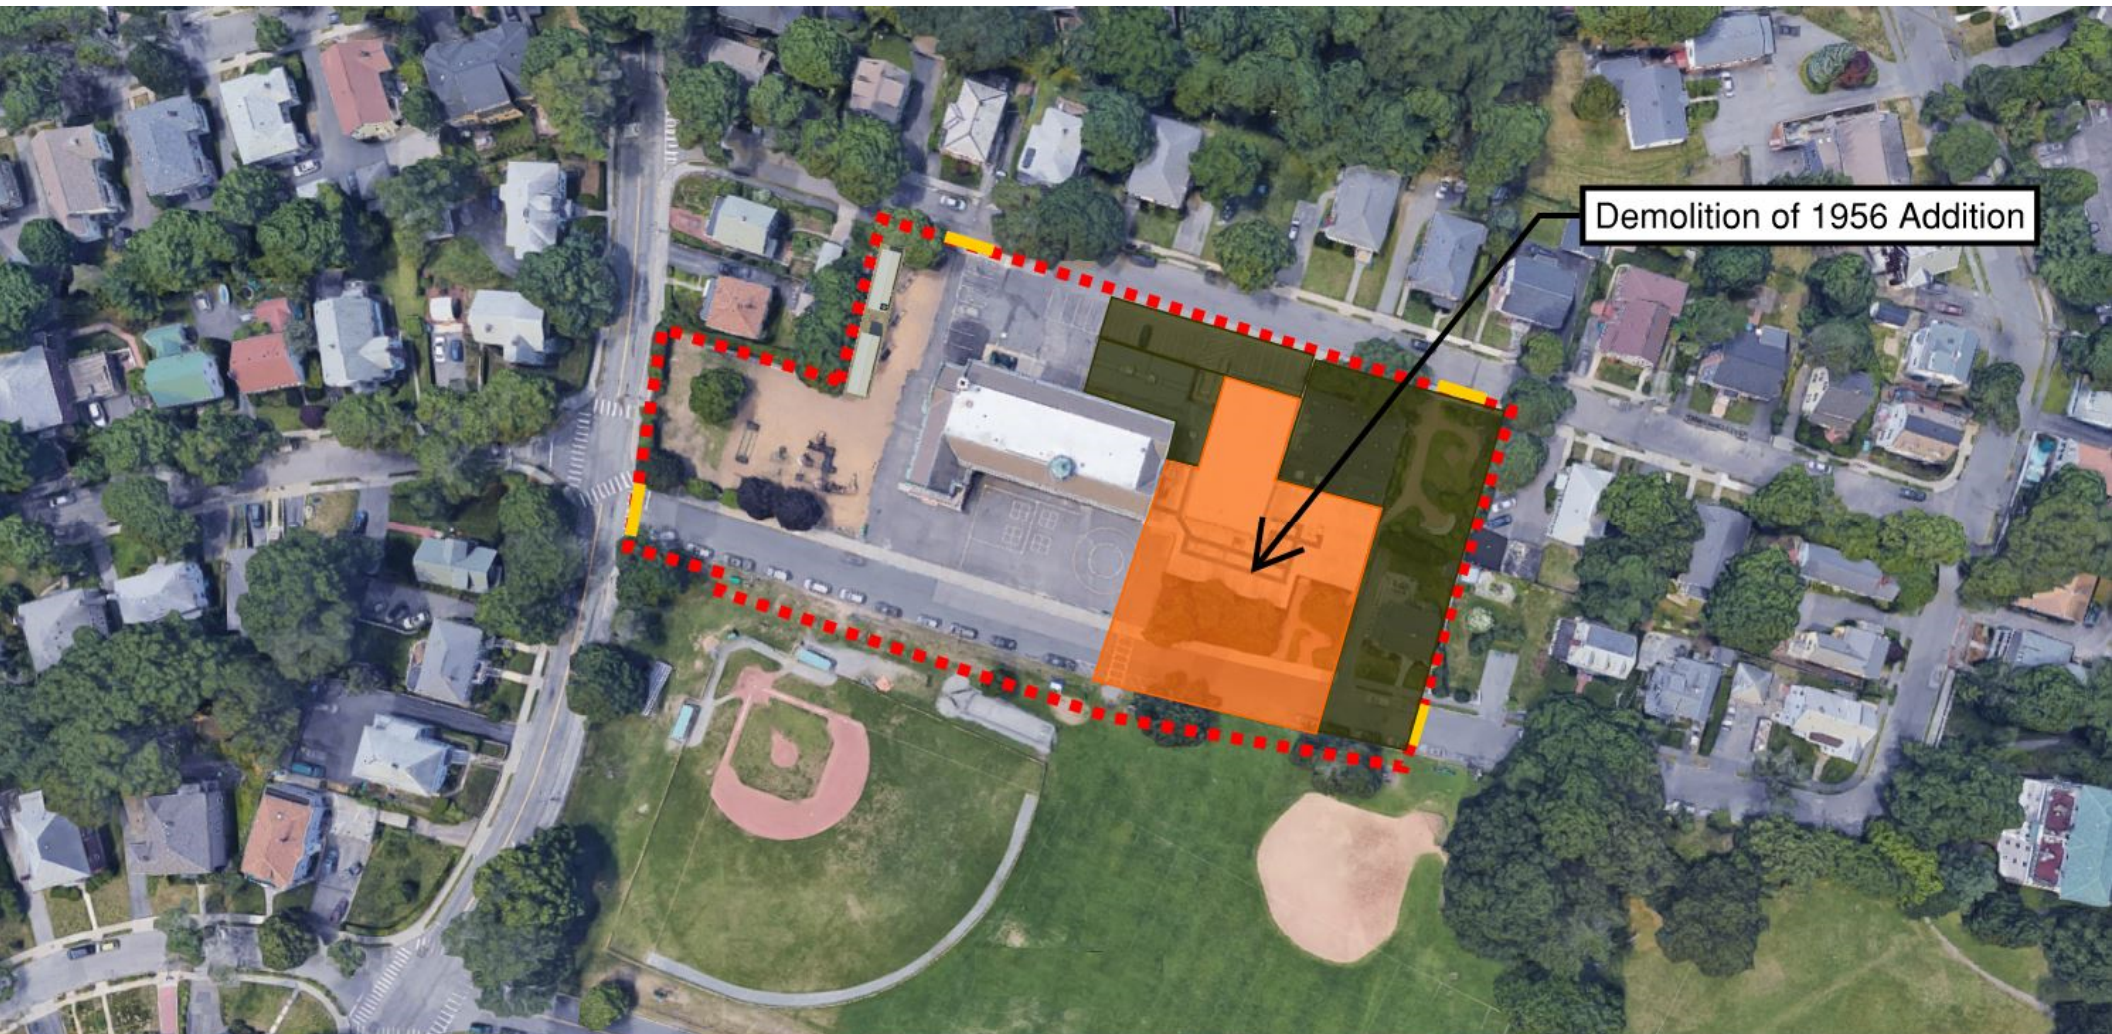

Demolition of 1956 Addition

Stage 3: Abatement & Selective Demo of 1929 Building and Site Demo

End of July 2017

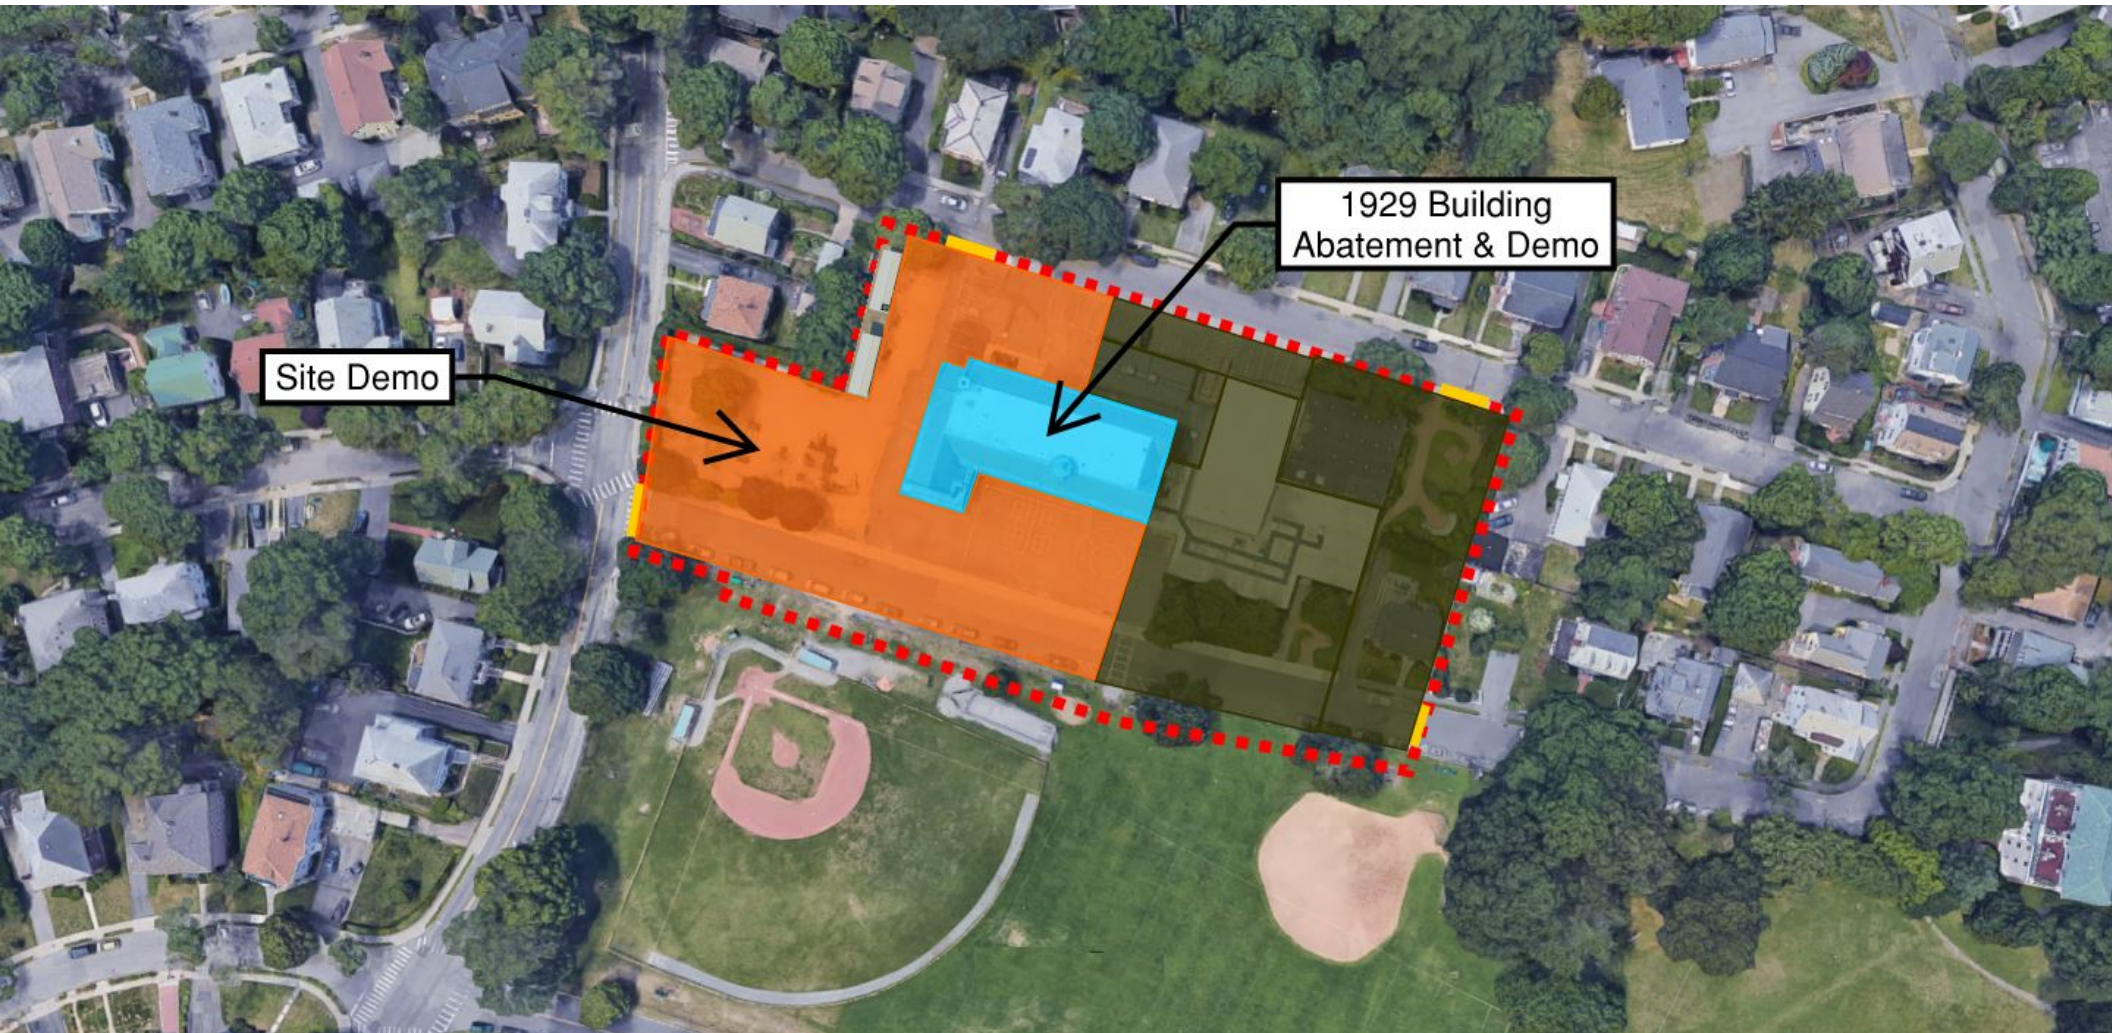

Stage 4: Bridges Ave Utility Work & Culvert Work


End of July 2017



Bridges Ave Utility
& Culvert Work

Stage 5: Library Foundation, Culvert Work, & Closing of Softball Field

Mid August 2017

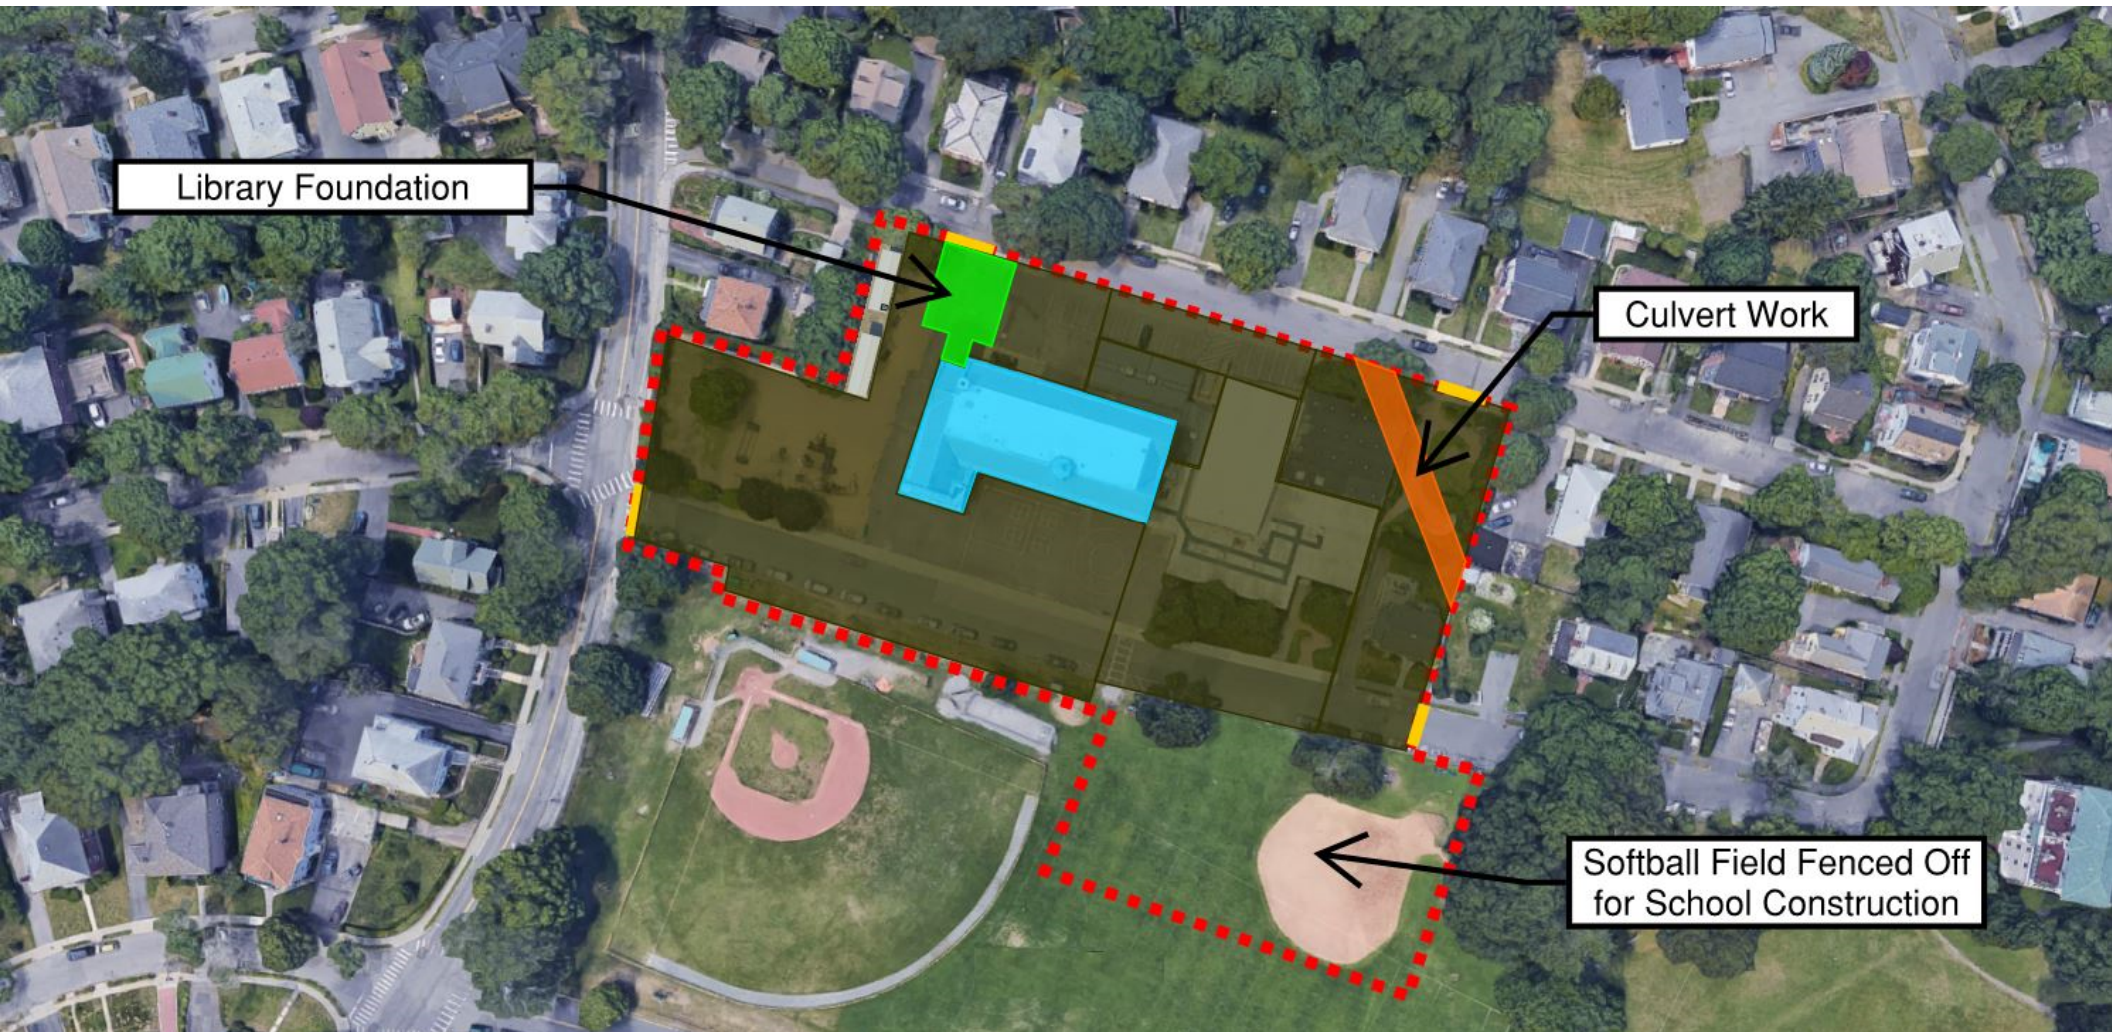

Stage 6: Classroom Foundation and Culvert Work

Late August 2017



Field Relocation: Construct New Softball Field & Future Paths

September 2017 – April 2018



Stage 7: Gym Foundation, Culvert Work, & Park Improvements

Mid October 2017




Stage 8: Library Structural Steel Erection and Culvert Work

Late October 2017



Stage 9: Classroom Steel Erection

Early December 2017

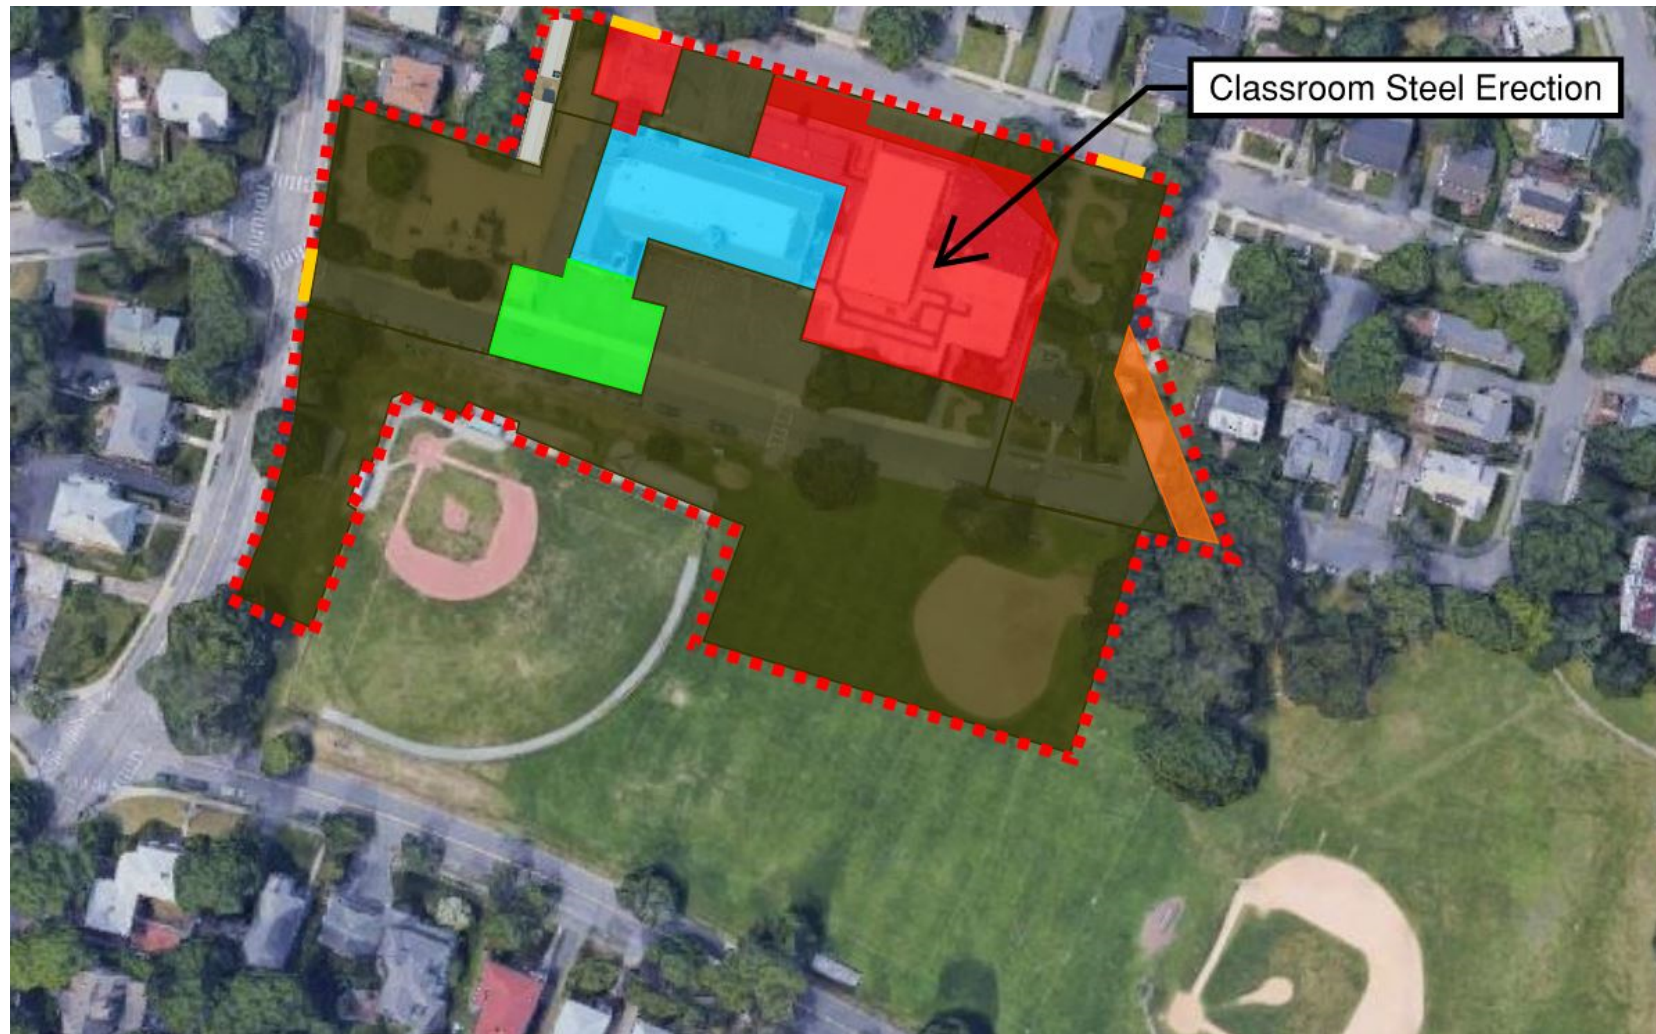

Stage 10: Gym Steel Erection

Early March 2018



Stage 11: Little League & Softball Activities Resume

April 2018

