

CABOT ELEMENTARY SCHOOL PROJECT

Community Update

Cabot Construction Project


Construction Sequencing Overview

Thursday, May 18, 2017 – 7:00PM
Cabot Gymnasium




W.T. RICH COMPANY, INC.

Site Circulation

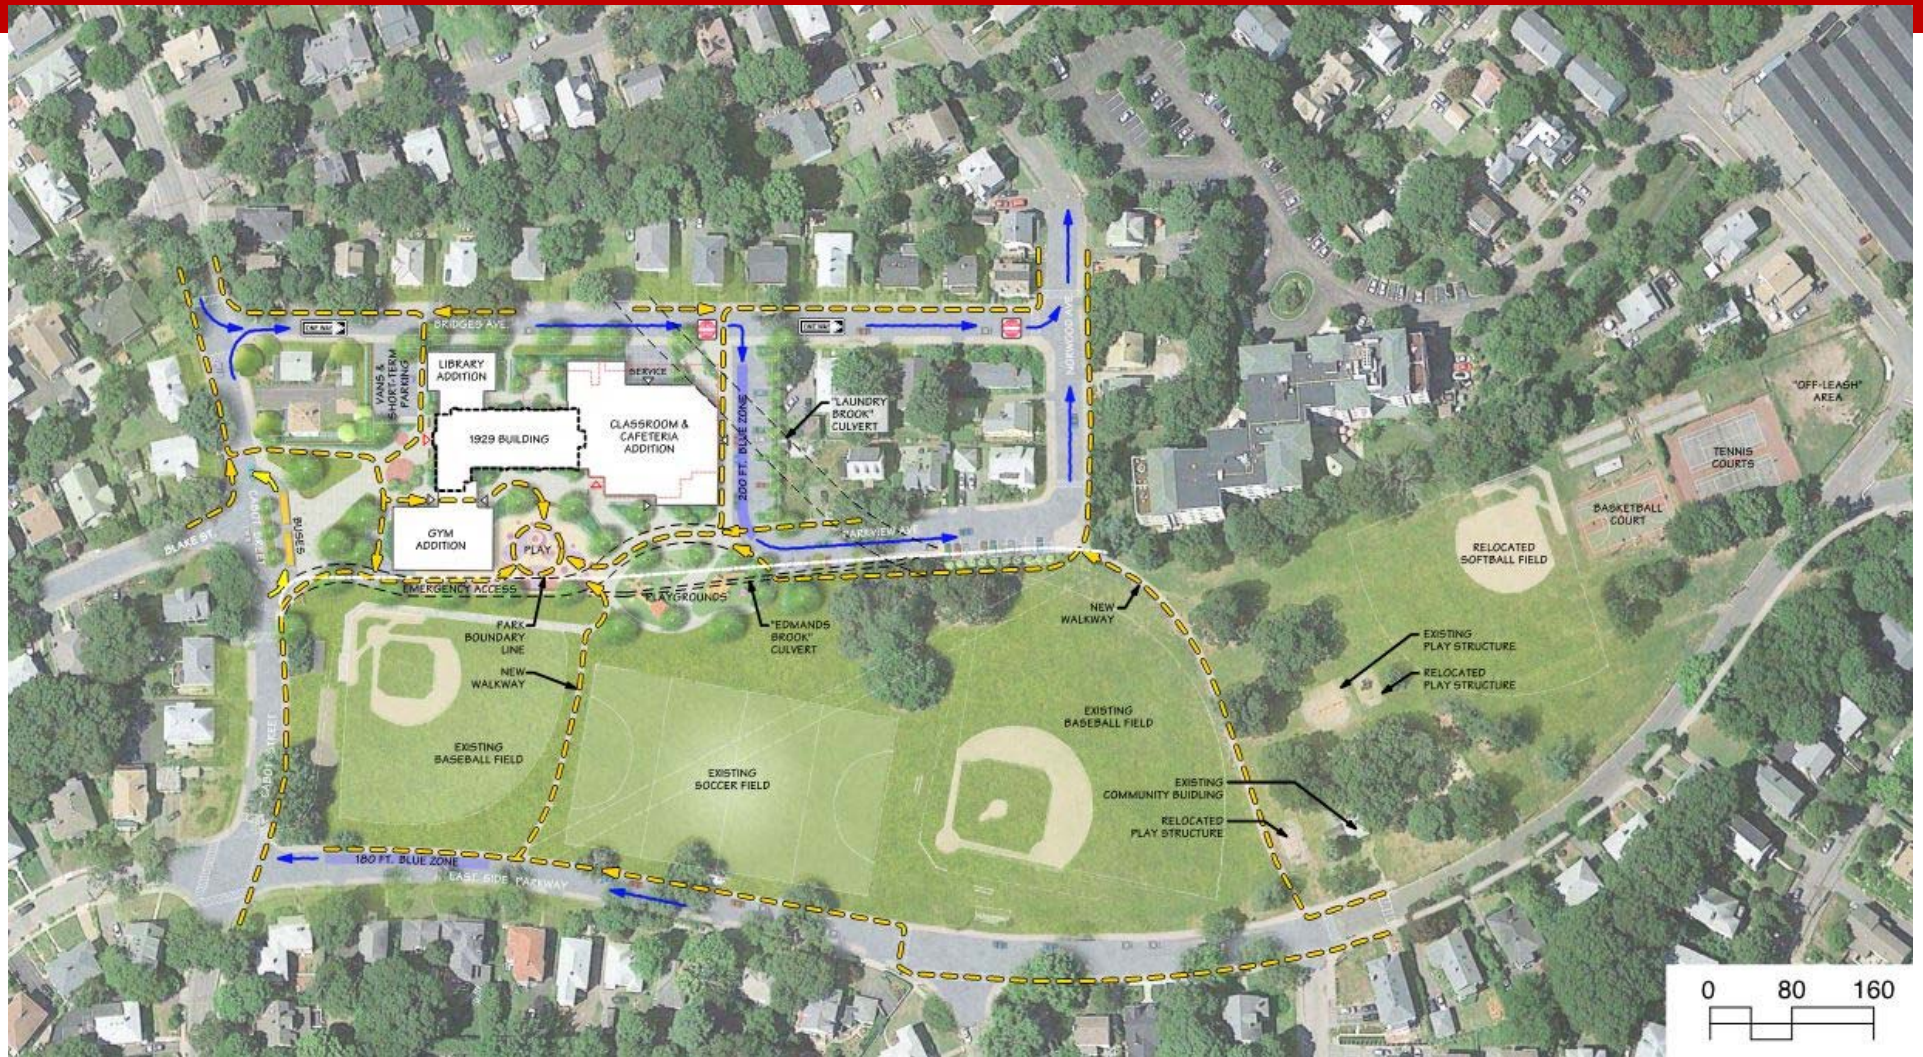


Traffic Signage: Setup Traffic Controls

Early July 2017

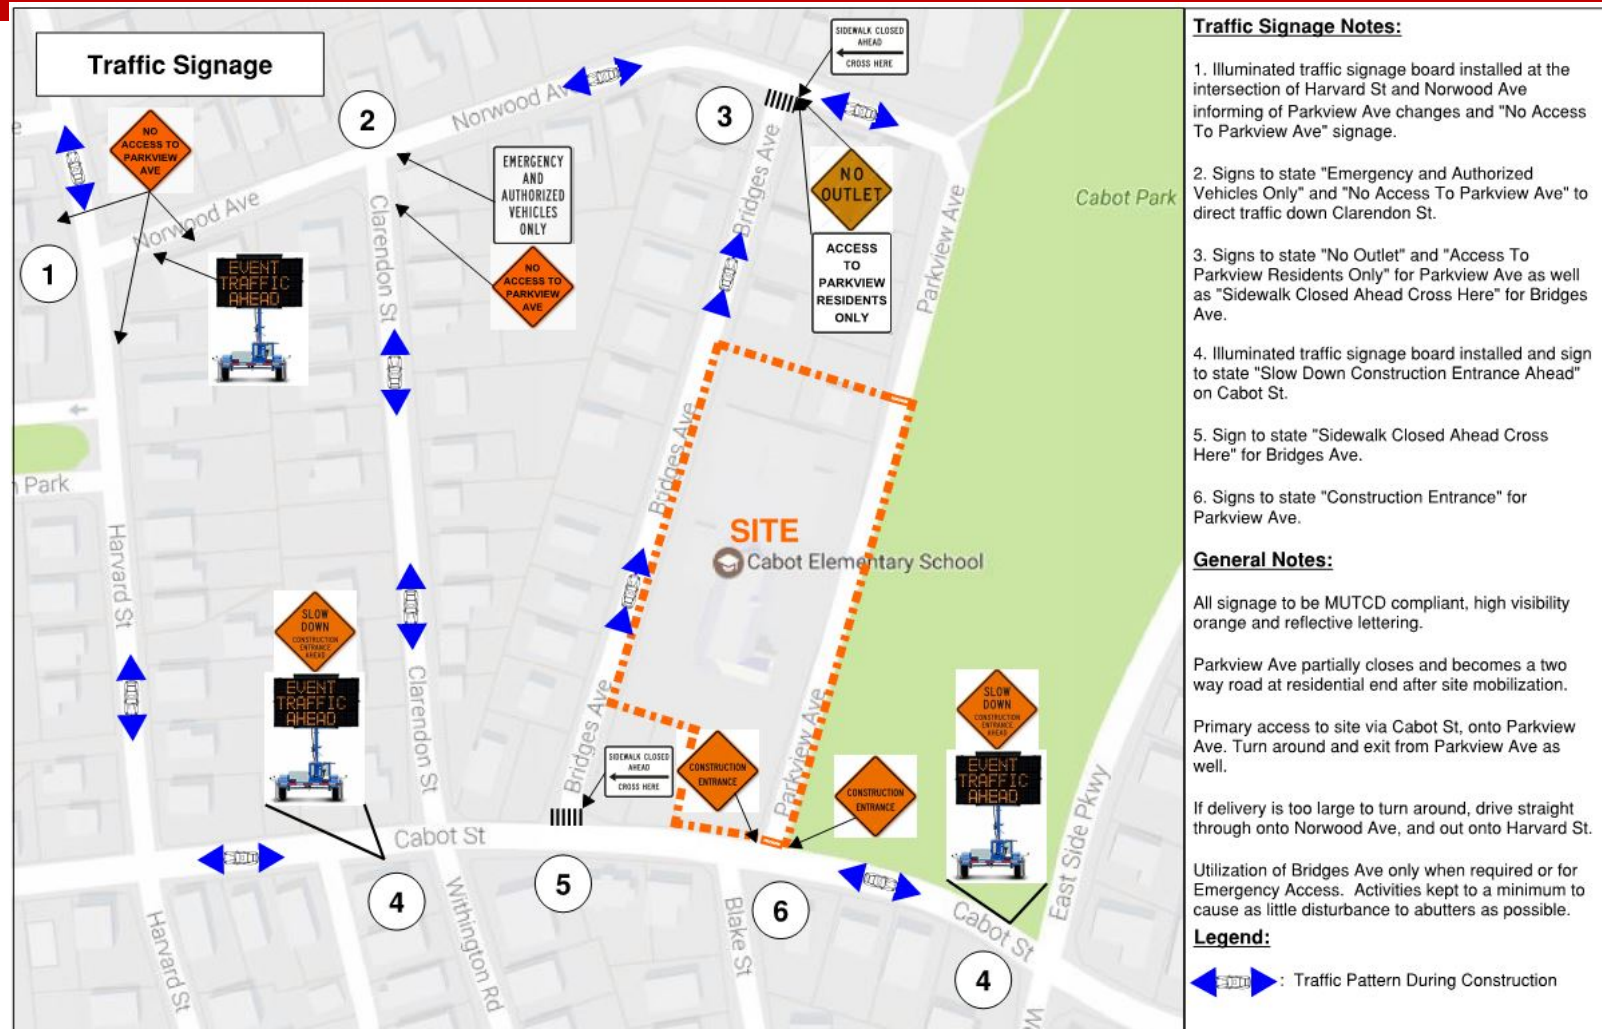


Site Mobilization: Setup Site Controls & Facilities

Early July 2017

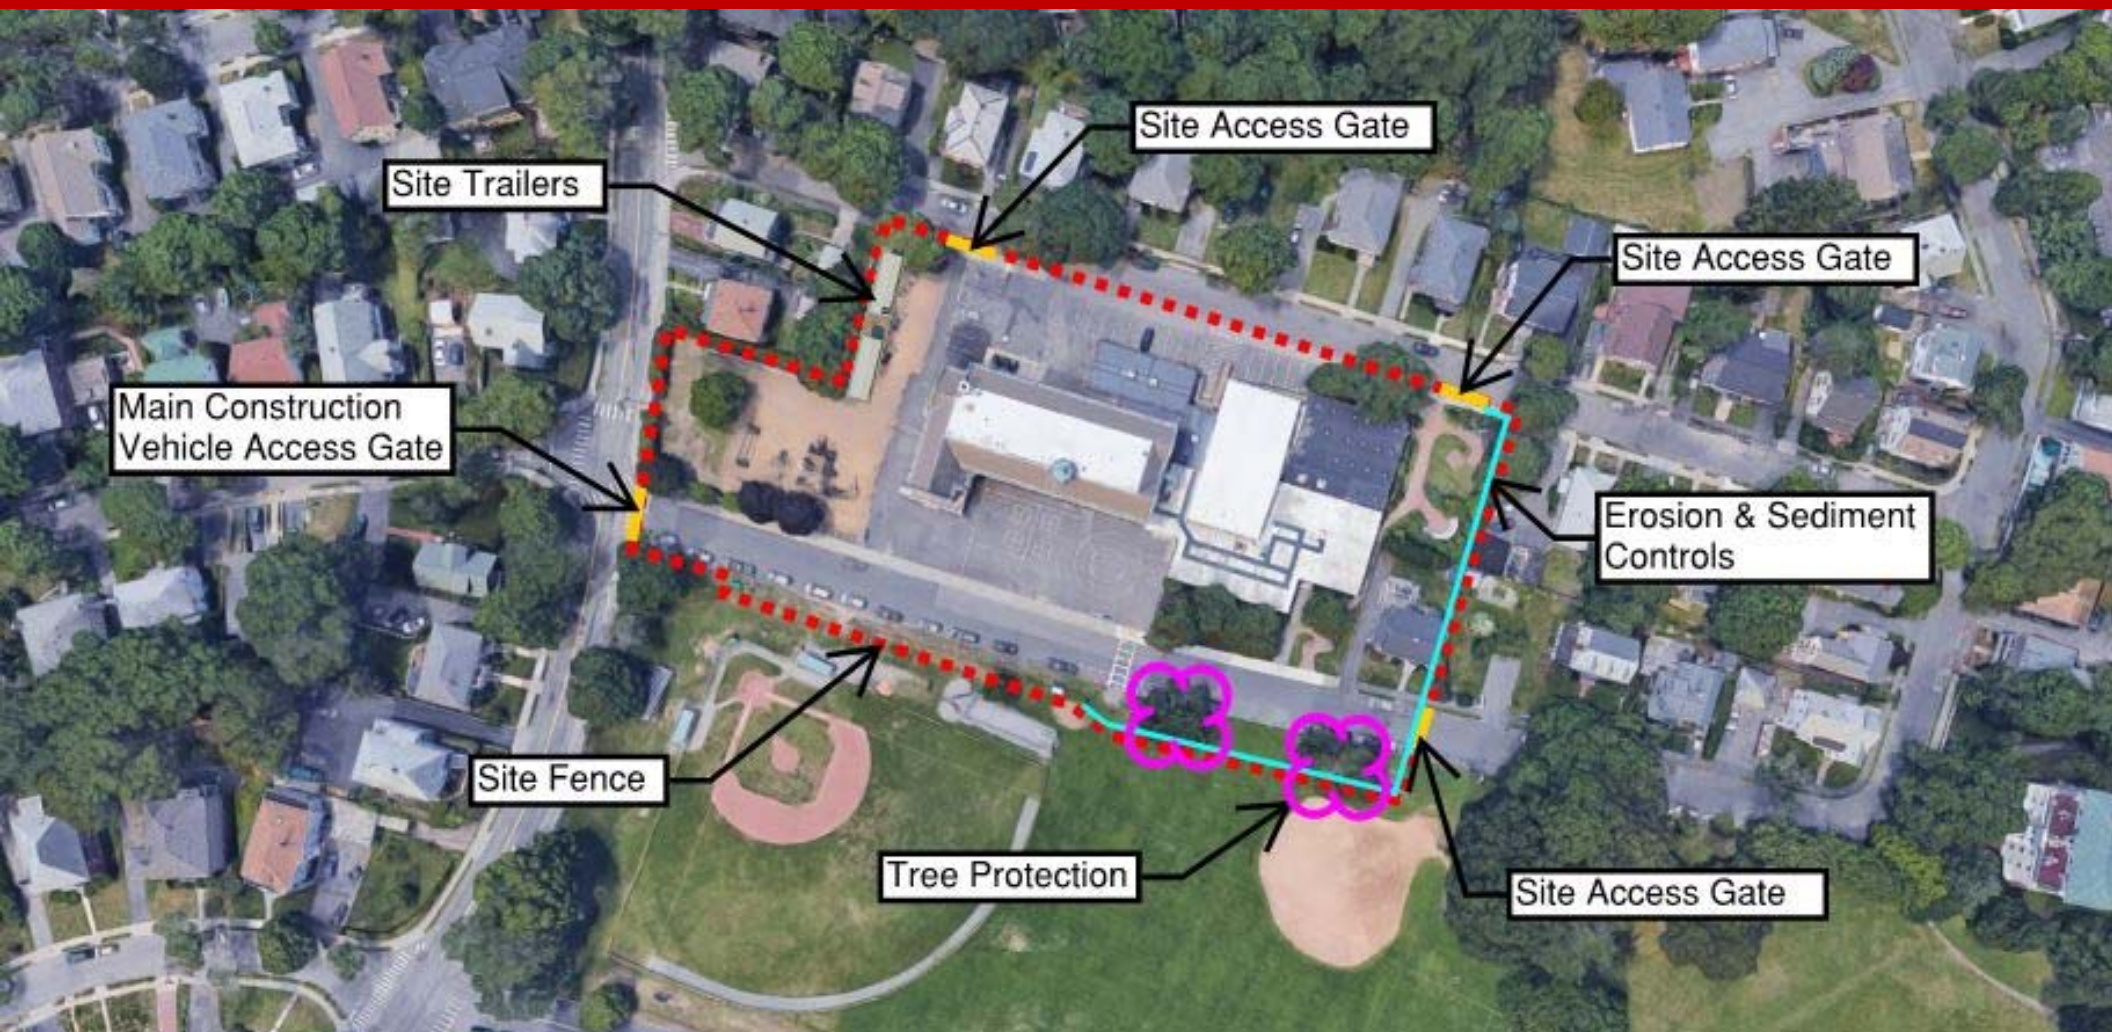

1


Demolition of Modular Classrooms, 23 Parkview, & Landscaping Early July 2017

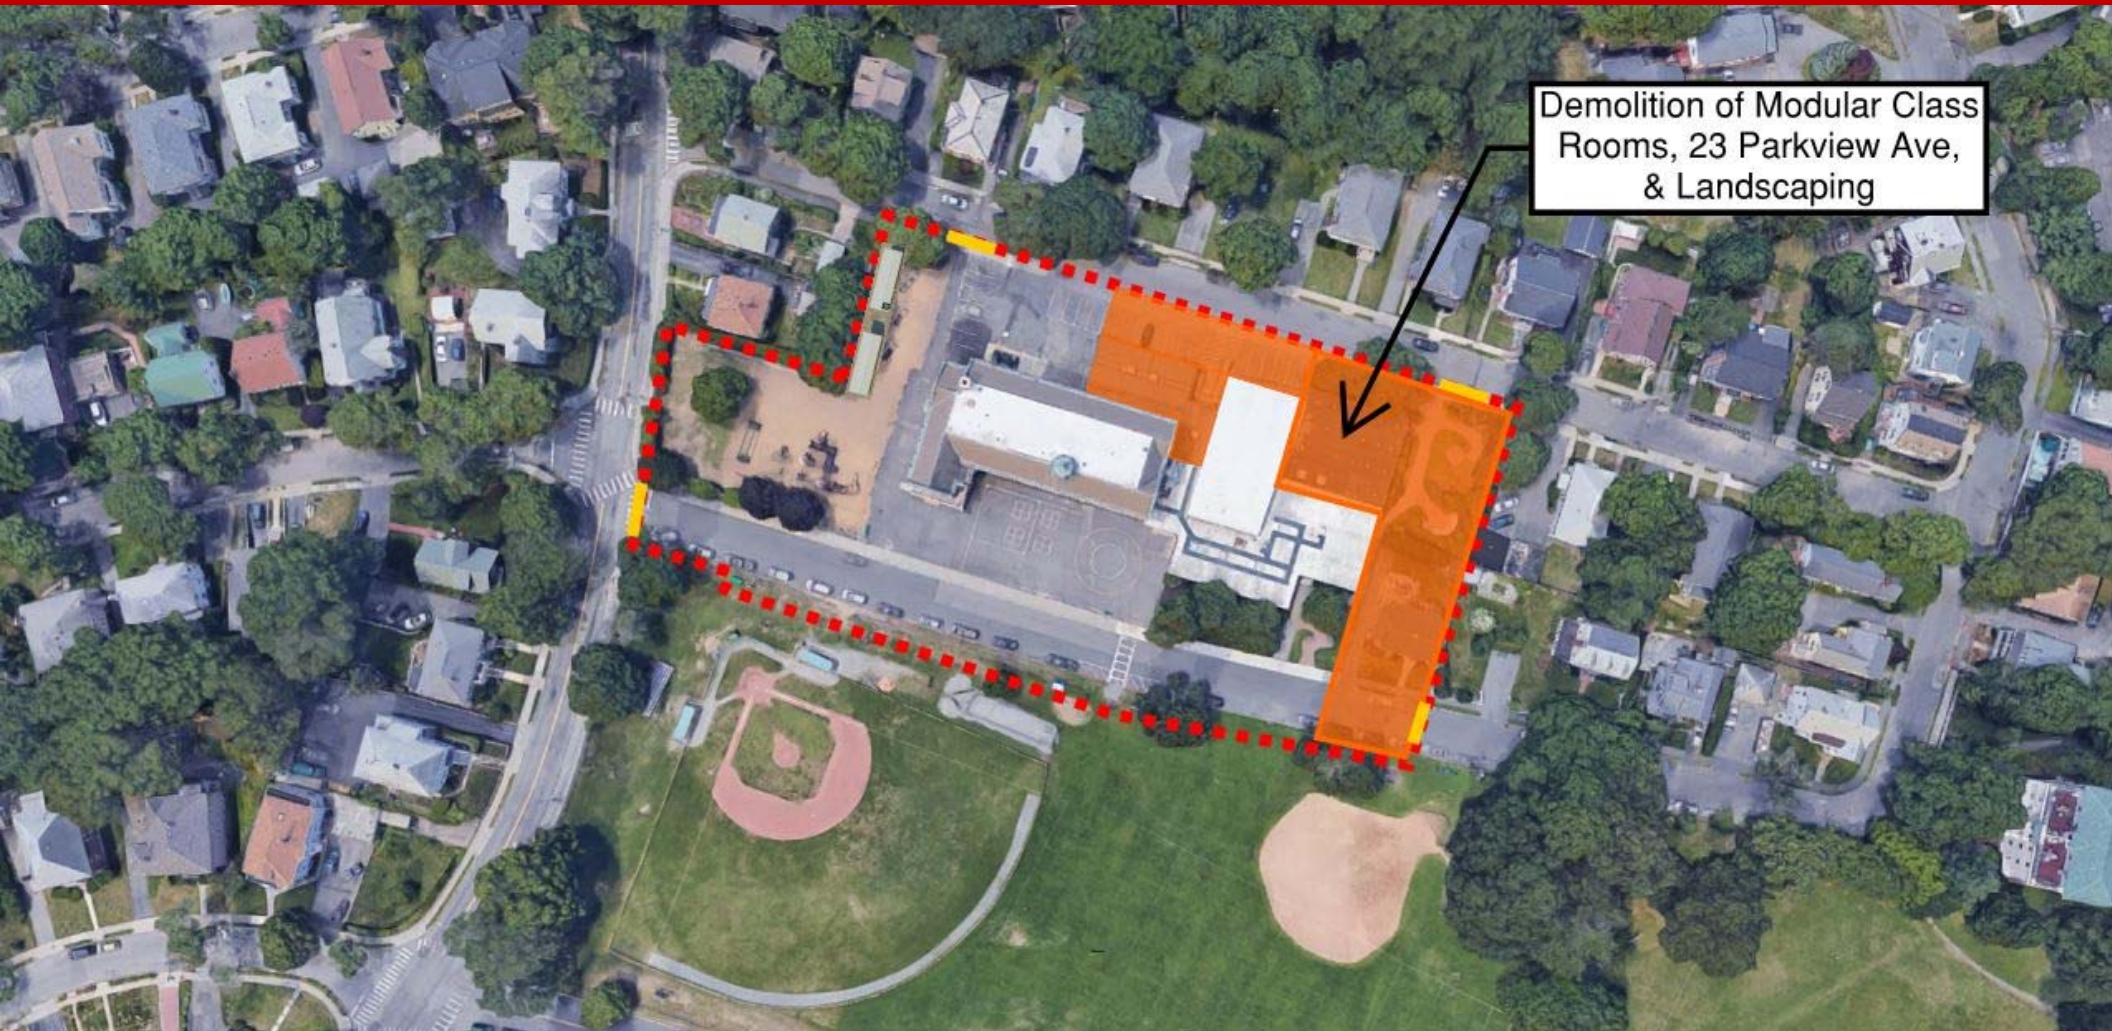

2

Demolition of 1956 Addition


Mid July 2017

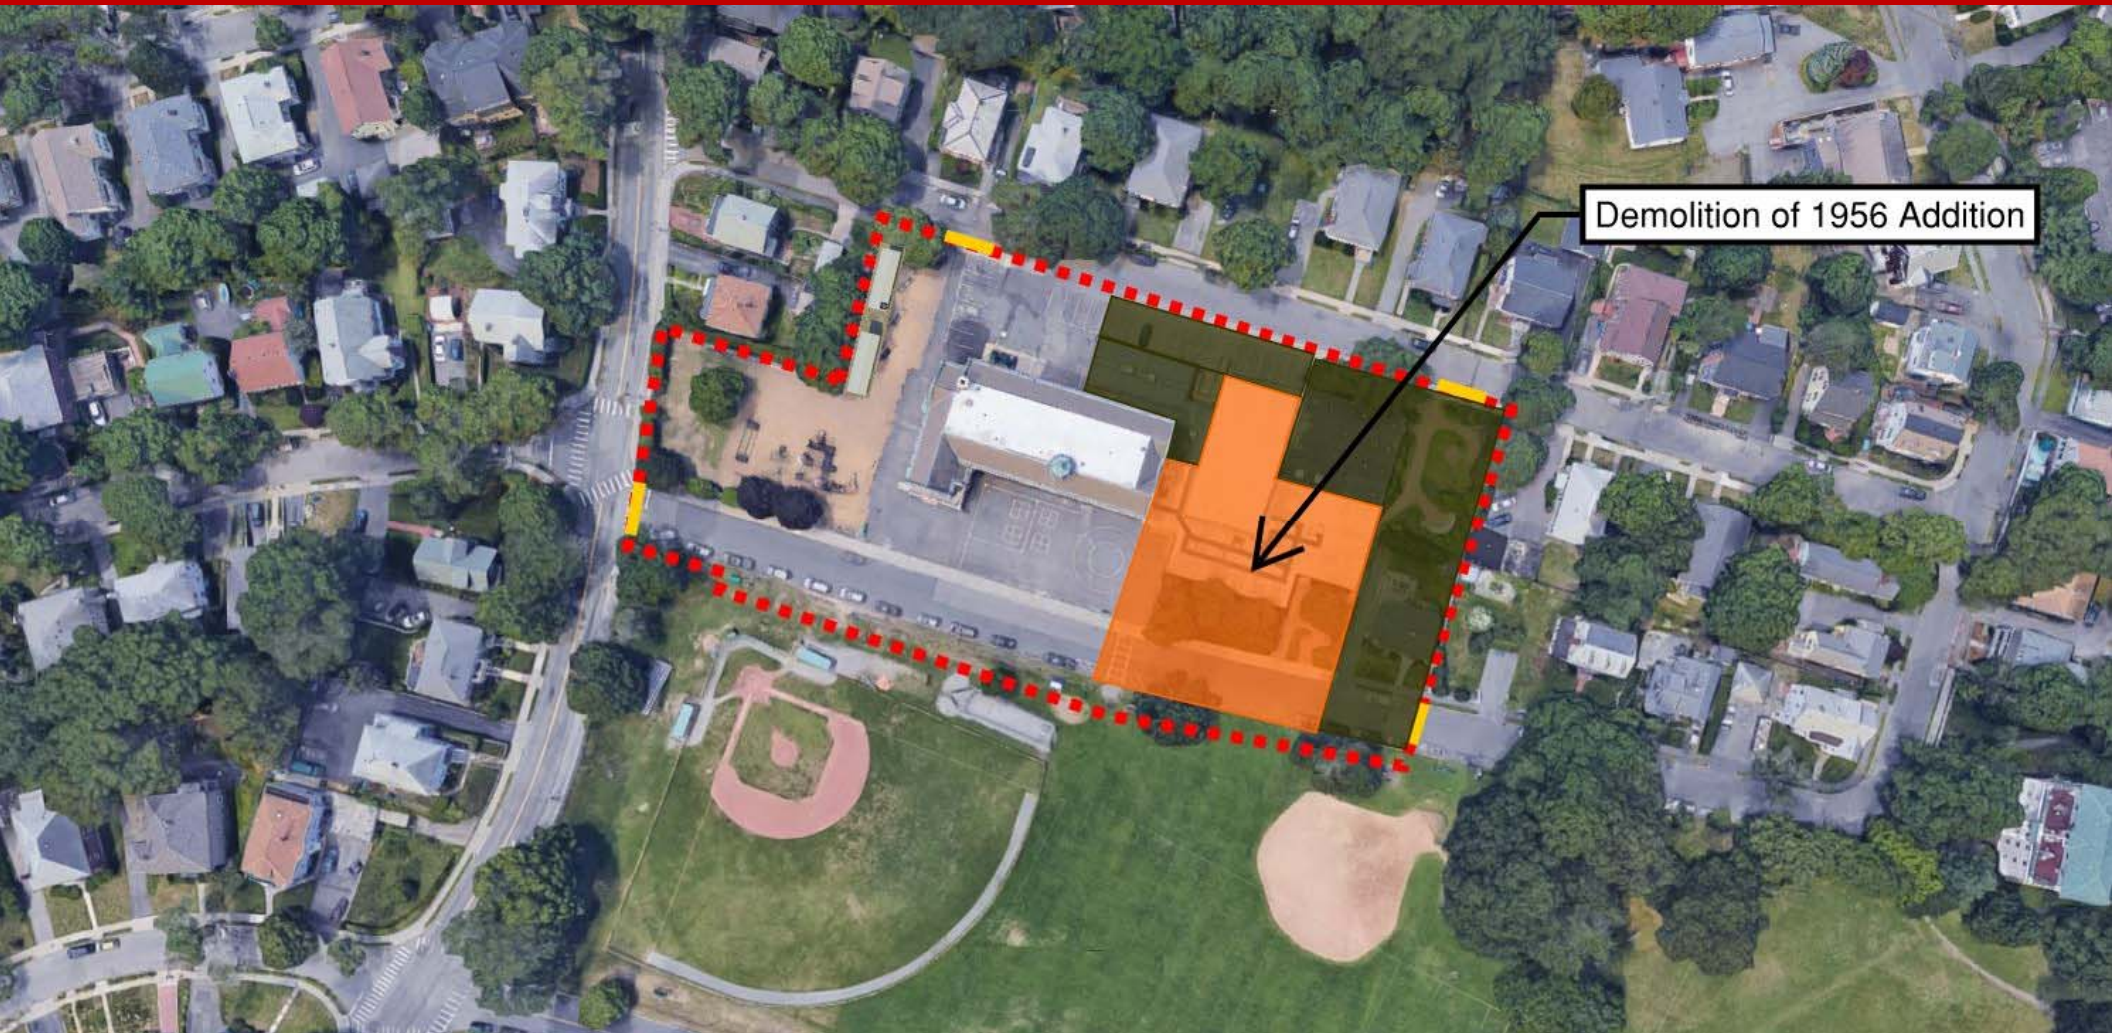

Demolition of 1956 Addition

3 Abatement & Selective Demo of 1929 Building and Site Demo

End of July 2017

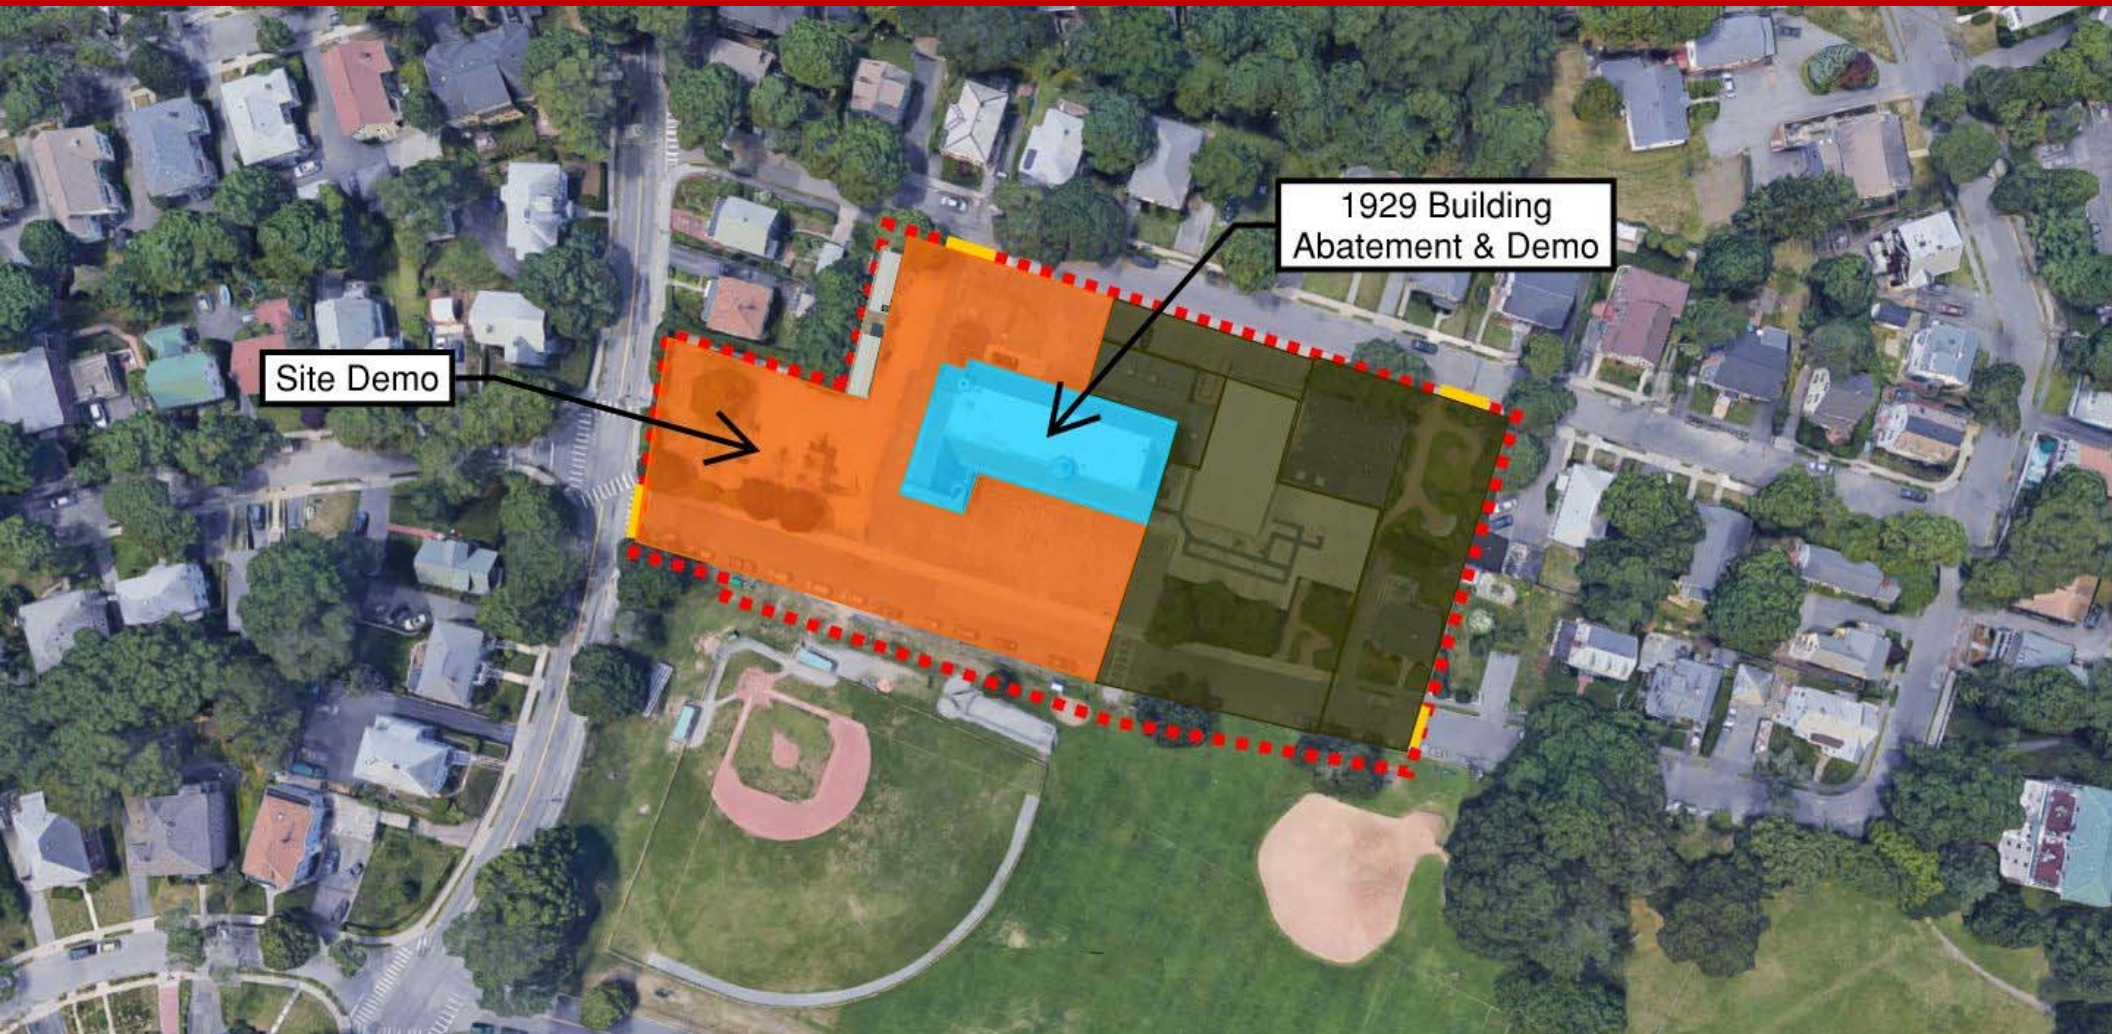

4

Bridges Ave Utility Work & Culvert Work


End of July 2017



5

Library Foundation, Culvert Work, & Closing of Softball Field

Mid August 2017

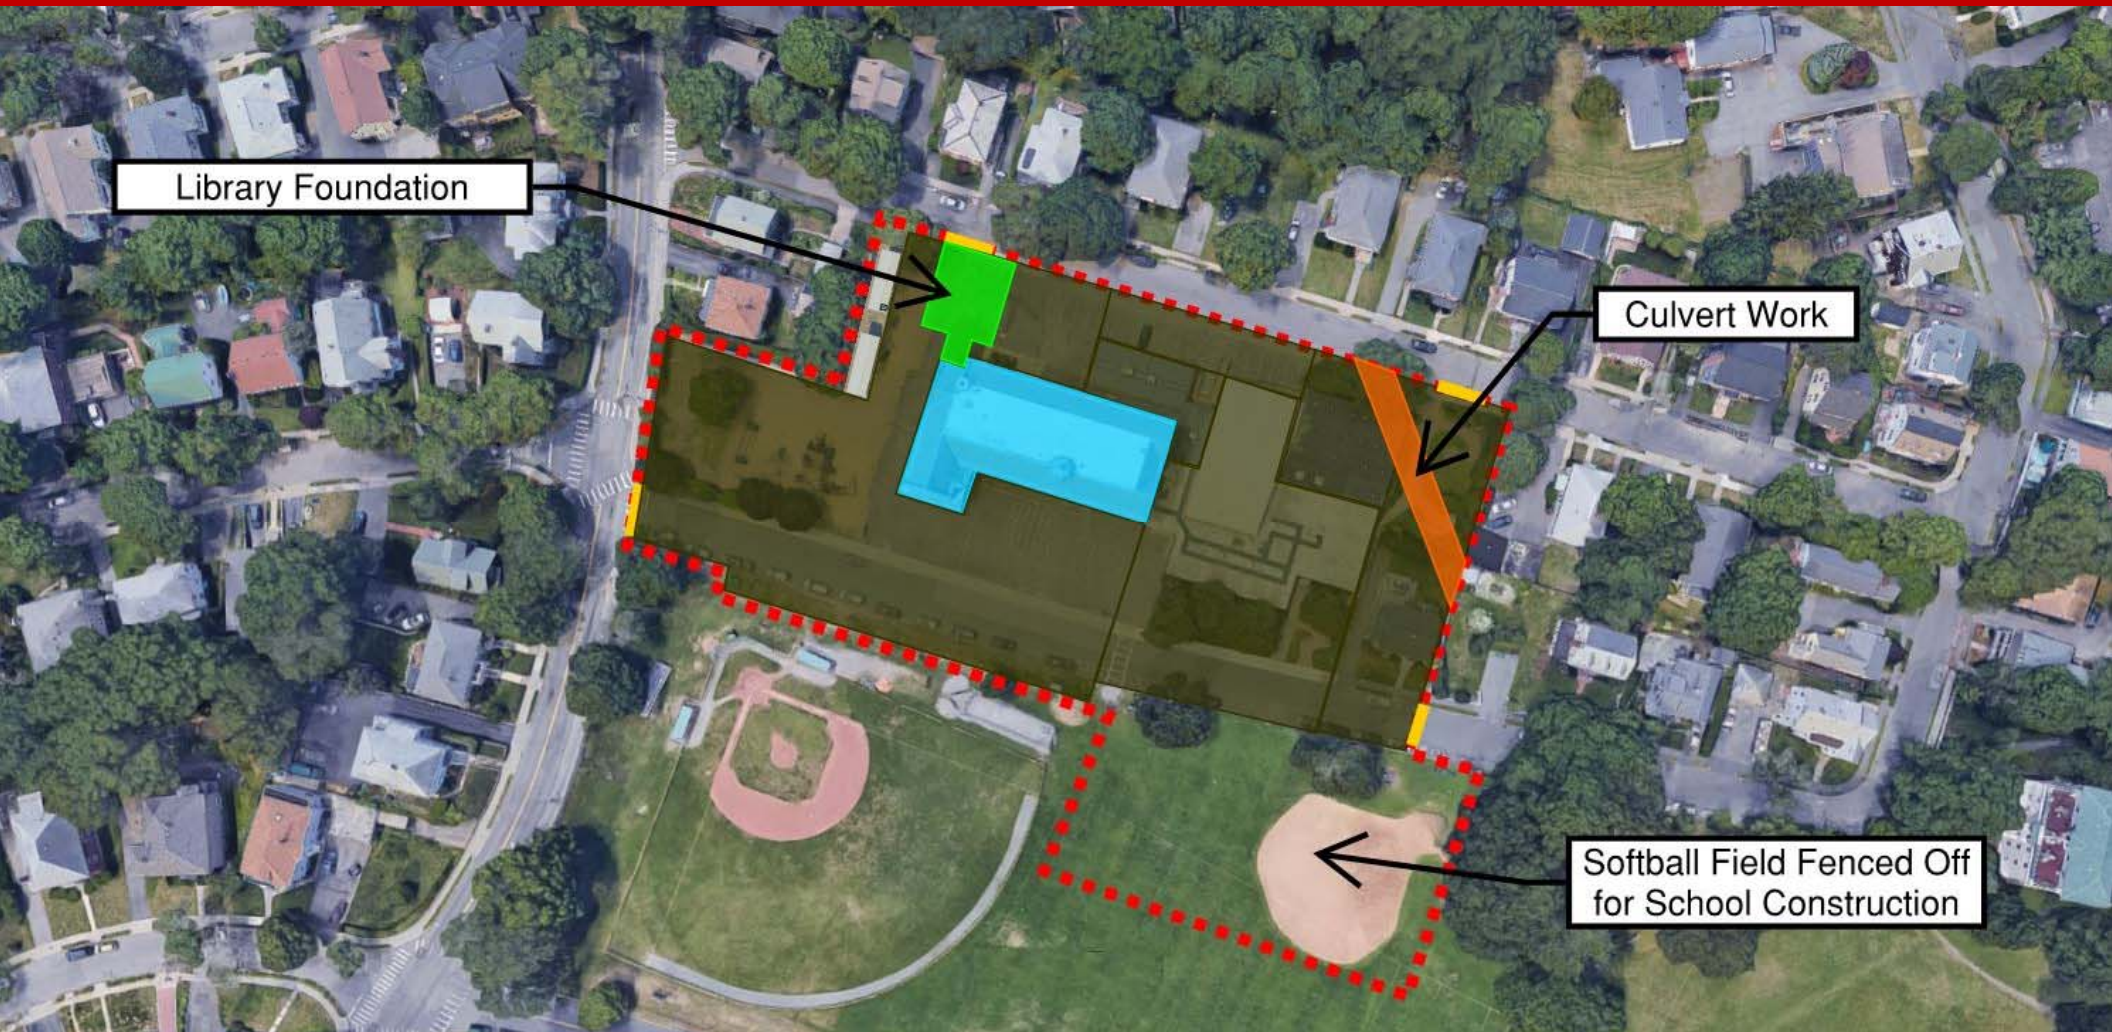

6

Classroom Foundation and Culvert Work

Late August 2017



Field Relocation: Construct New Softball Field & Future Paths

September 2017 – April 2018



7

Gym Foundation, Culvert Work, & Park Improvements Mid October 2017




Library Structural Steel Erection and Culvert Work

Late October 2017



Classroom Steel Erection


Early December 2017

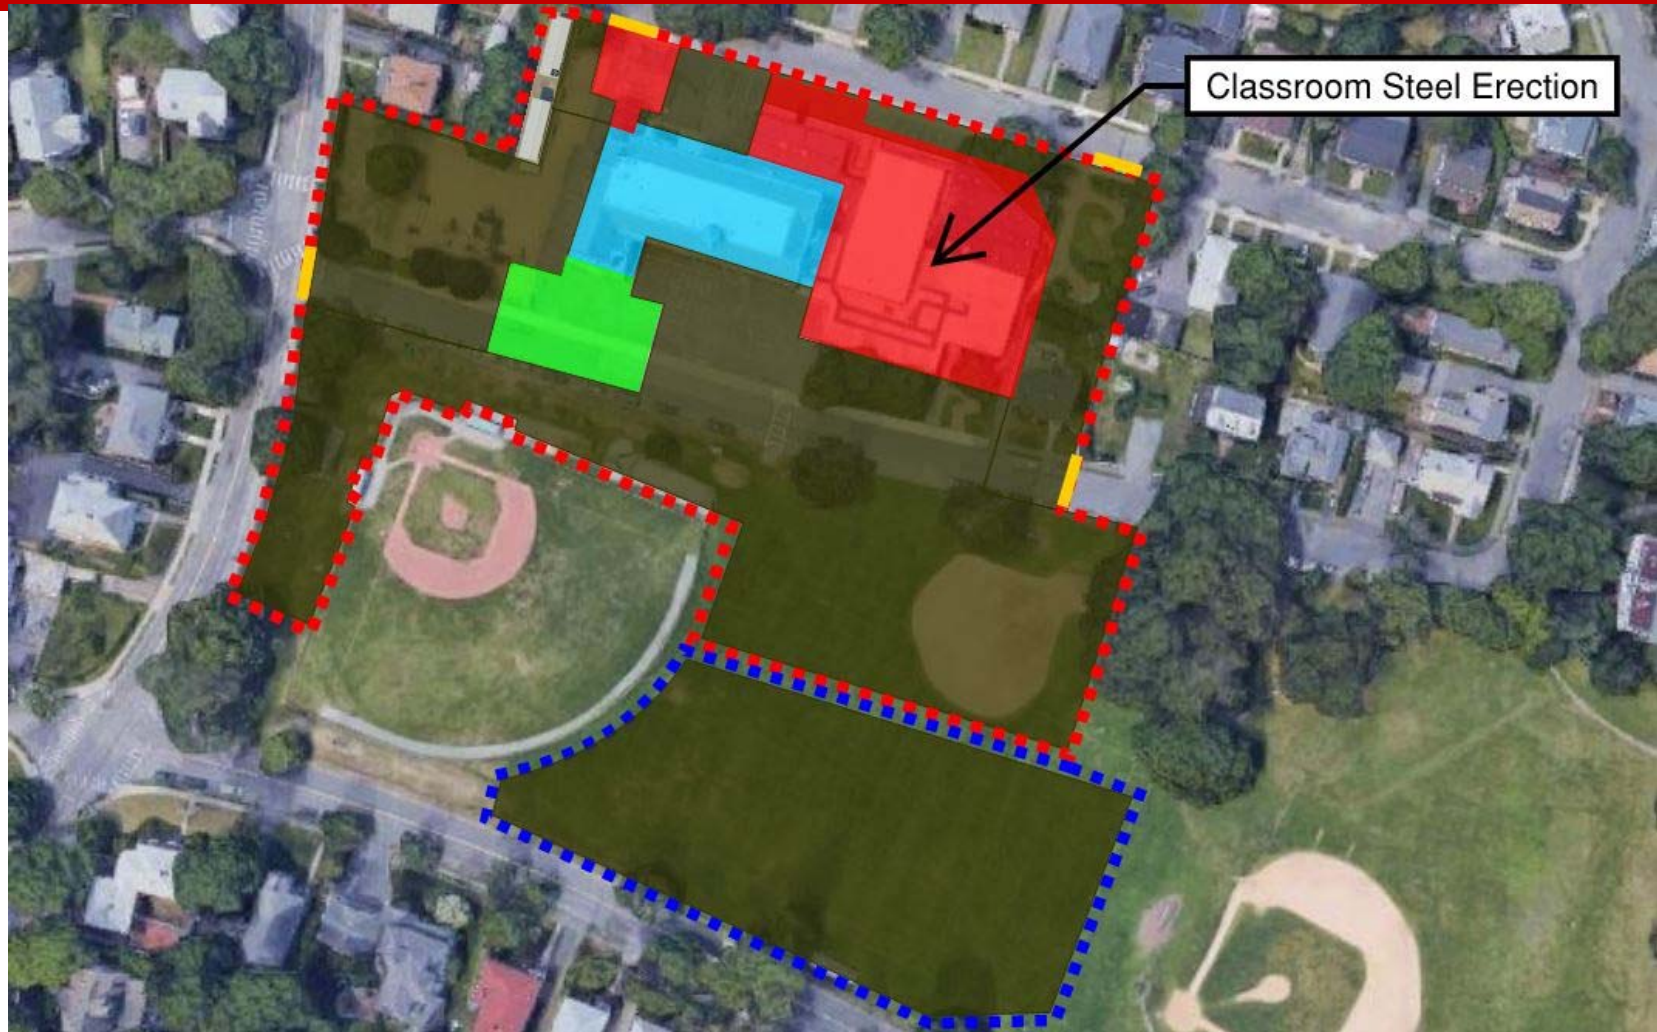

10

Gym Steel Erection

Early March 2018

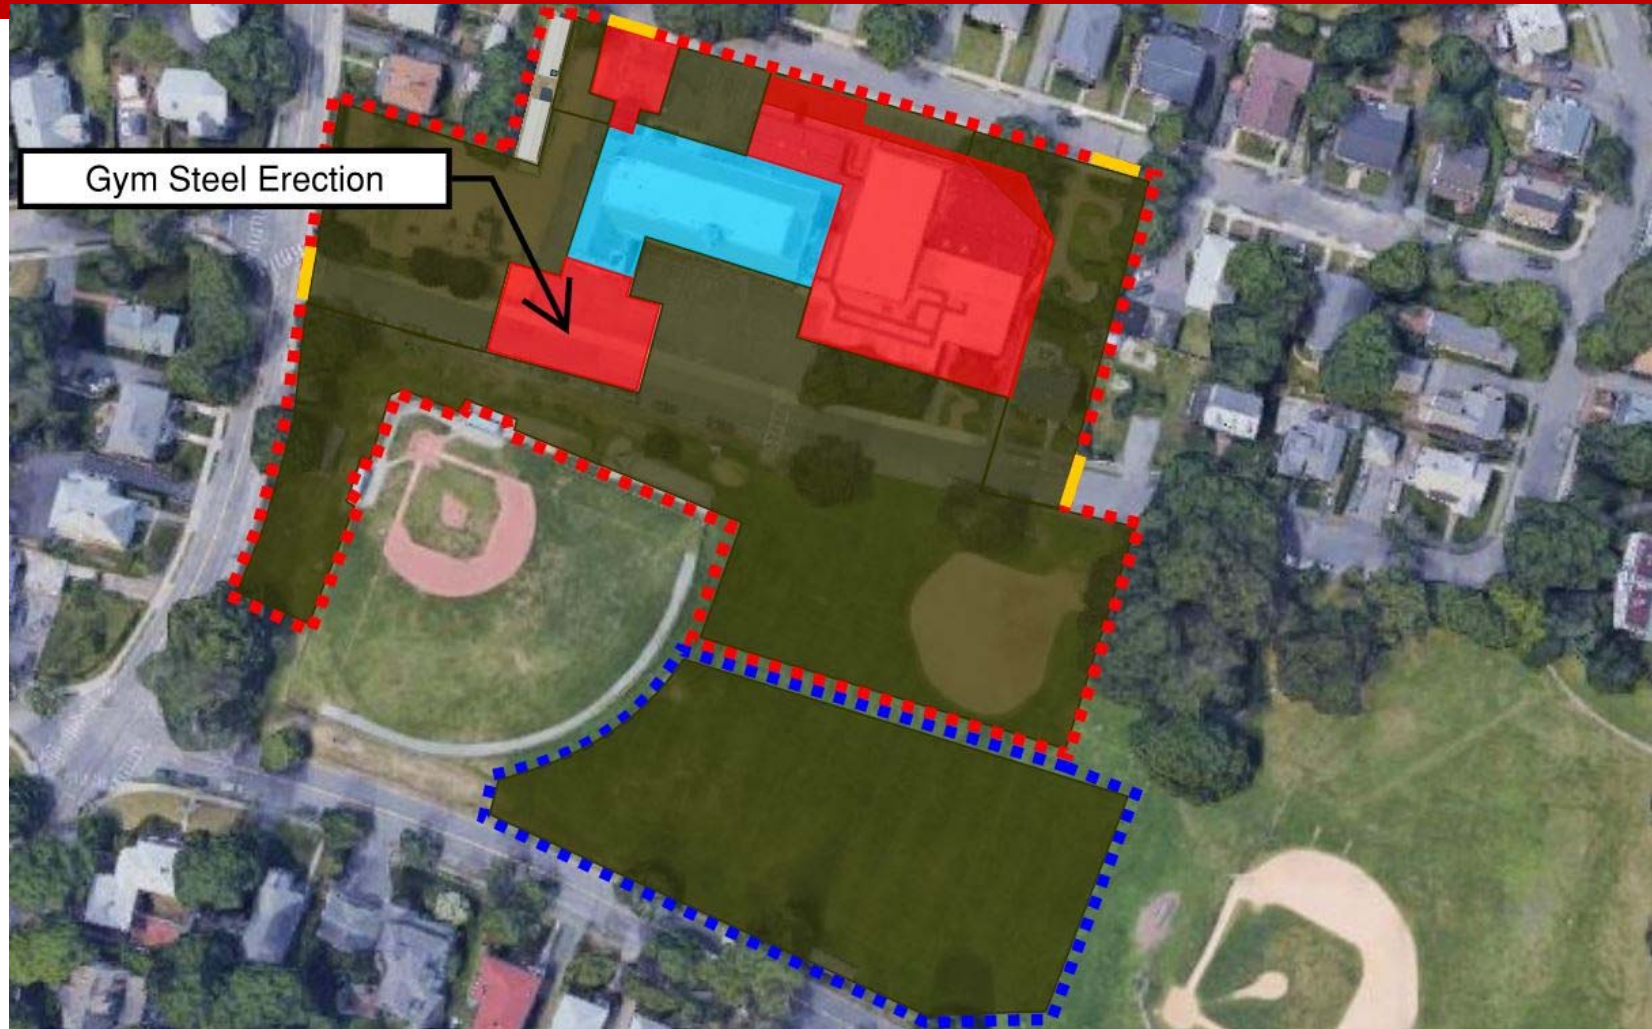

Little League & Softball Activities Resume

April 2018



CABOT ELEMENTARY SCHOOL PROJECT

For project information, and to track updates throughout the process, including upcoming meetings, please visit:

http://www.newtonma.gov/gov/building/capital_projects/cabot_school/

Please submit contact information on this website if you would like to receive future meeting notifications by e-mail.

For general project inquiries, please contact:
Alex Valcarce, City of Newton Project Manager at
(617) 796-1600
